

SPECTRUMPC.COM

APPROVED
by Aaron Cypher 09/08/2021

Spectrum Design Project No.: 19106



SHEET ISSUE DATE:
07.30.2021


REVISION	NUMBER	DATE
----------	--------	------

KEY PLAN:

SHEET NAME:


SHEET NUMBER:

C401-3

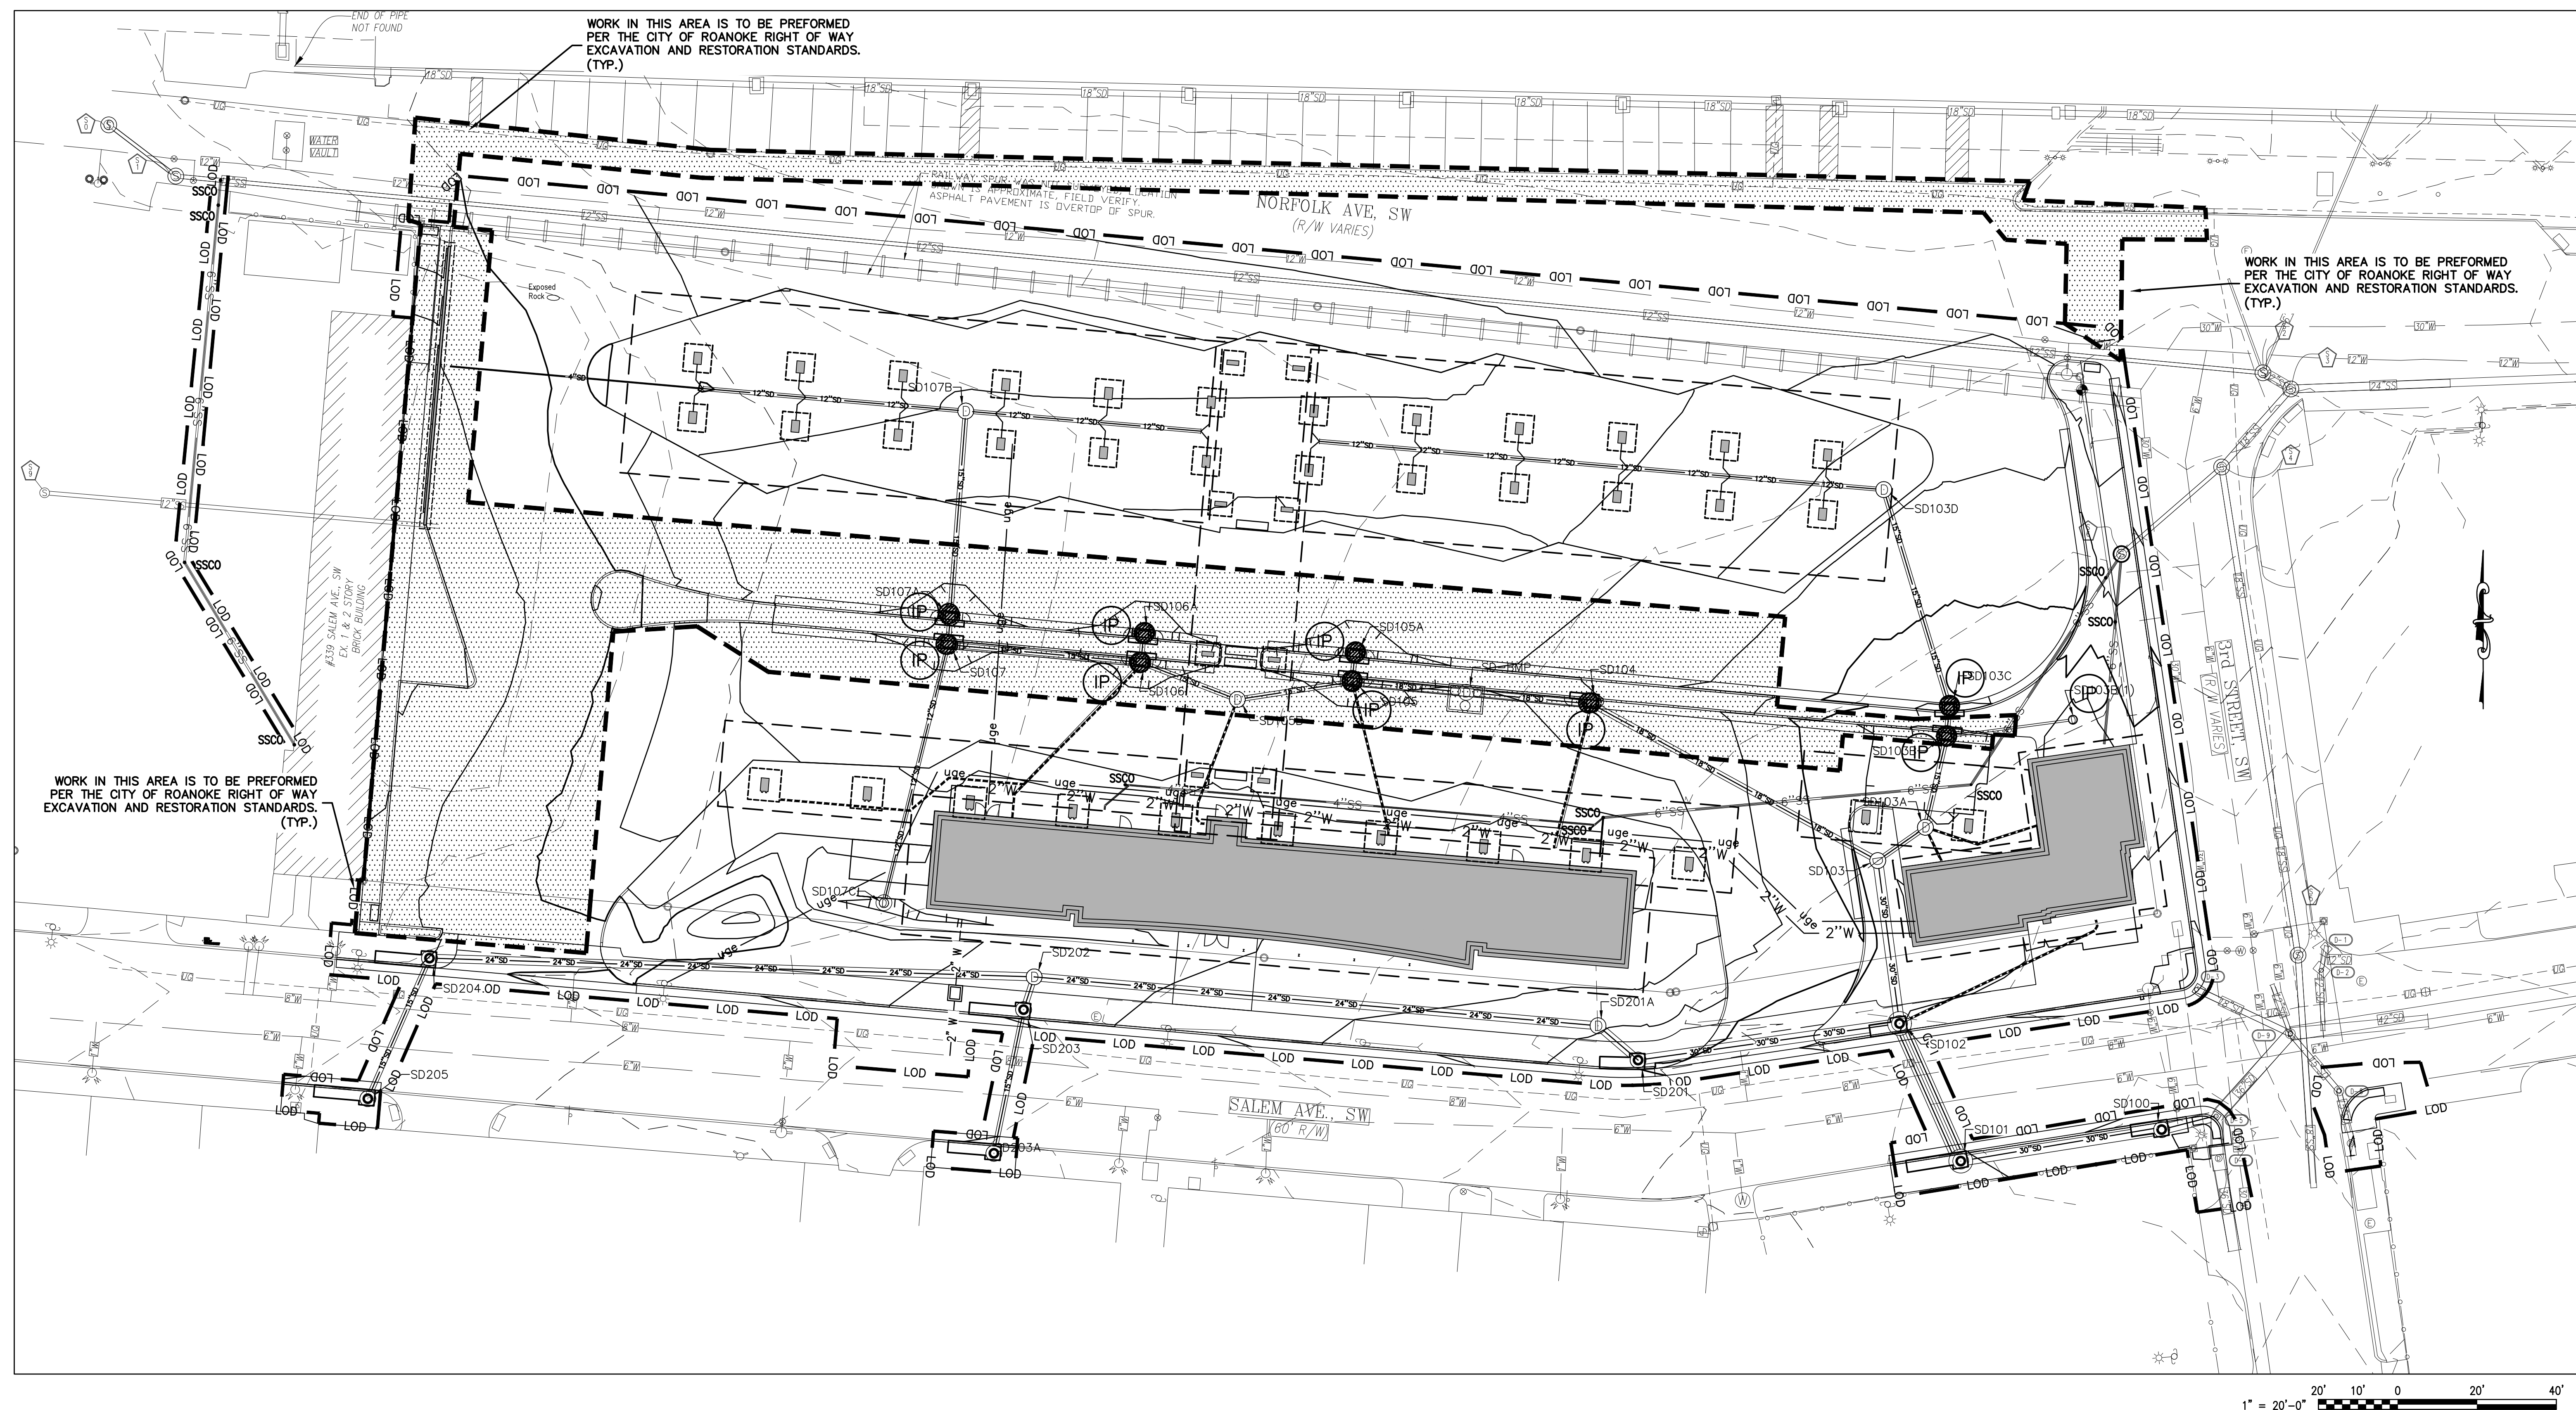

STAGE 3 - SEQUENCE OF CONSTRUCTION

1. REMOVE STAGE CONSTRUCTION STRUCTURES AND UTILIZE PAVED ENTRANCES ALONG SALEM AVE. FOR ENTRY/EXIT. MONITOR SURFACES FOR CLEANLINESS FOR ANY REMAINING ACTIVITY.
2. INSTALL INLET PROTECTION AT ALL NEW STORM STRUCTURES (OR MODIFIED STRUCTURES) IN THIS PHASE.
3. REMOVE INLET PROTECTION MEASURES AT STRUCTURES WHERE UPSTREAM AREAS HAVE RECEIVED PERMANENT ASPHALT OR CONCRETE.
4. INLET PROTECTION AT SD103B(1) SHALL REMAIN UNTIL CONTRIBUTING LAWN IS STABILIZED WITH GRASS.
5. REMOVE REMAINING ESC MEASURES.
6. CONFIRM APPROVAL WITH CITY ESC (INSPECTOR) PRIOR TO REMOVAL OF ANY ESC MEASURES.

ESC LEGEND	
PROPOSED	DESCRIPTION
	STORM DRAIN INLET PROTECTION VA ESC HANDBOOK No. 3.07
	STAGE AREA
	LIMITS OF DISTURBANCE

SEE VIRGINIA EROSION & SEDIMENT CONTROL HANDBOOK
