



E.S.C. PHASE II CONSTRUCTION SEQUENCE:

1. THE SWPPP SHALL BE PROVIDED ON-SITE AND ALL REGULATIONS, INSPECTIONS, AND PROCEDURES FOLLOWED FOR THE ENTIRE DURATION OF THE PROJECT. SEE GENERAL PERMIT DETAILS FOR ADDITIONAL INFORMATION AND SWPPP FOR SITE SPECIFIC REQUIREMENTS AND INSPECTIONS.
 2. THE SILT FENCE SHALL BE MAINTAINED THROUGHOUT THE DURATION OF THE PROJECT.
 3. THE CONCRETE WASHOUT SHALL BE INSTALLED AND MADE FUNCTIONAL PRIOR TO ANY CONCRETE INSTALLATION ON-SITE.
 4. DIVERSION DIKES SHALL BE REMOVED AS THE CURBING IS CONSTRUCTED AS RUNOFF WILL BE CONVEYED TO THE SEDIMENT TRAP. SEDIMENT TRAP SHALL REMAIN OPERATIONAL UNTIL THE ON-SITE STORM SEWER SYSTEM IS FUNCTIONAL. THE ROANOKE CITY INSPECTOR SHALL PROVIDE AUTHORIZATION FOR ANY E.S.C. REMOVAL PRIOR TO THE CONTRACTOR REMOVING THE MEASURE FROM THE SITE.
 5. PAVEMENT, CURBING, LANDSCAPING, ETC. SHALL BE INSTALLED AT THIS TIME. THE CONCRETE WASHOUT SHALL BE UTILIZED IN ACCORDANCE WITH D.E.Q. REGULATIONS.
 6. PERMANENT SEEDING AND MULCHING SHALL BE APPLIED AT THIS TIME TO ALL AREAS AT FINAL GRADE. BLANKET MATTING SHALL BE APPLIED TO ANY SLOPES 3:1 OR GREATER.
 7. ONCE THE MAJORITY OF UPSTREAM AREAS ARE STABILIZED, THE STORMWATER MANAGEMENT FACILITY SHALL BE CONVERTED TO ITS PERMANENT OUTLET CONFIGURATION.
 8. AFTER FINAL SITE STABILIZATION AND ROANOKE CITY APPROVAL, SILT FENCE, INLET PROTECTION, AND THE CONSTRUCTION ENTRANCE CAN BE REMOVED.
- *NOTE: ROANOKE CITY INSPECTION AND APPROVAL IS REQUIRED PRIOR TO THE REMOVAL OF EROSION AND SEDIMENT CONTROL MEASURES.
9. G.C. SHALL ENSURE THAT THE LIMITS OF DISTURBANCE ARE STRICTLY ADHERED TO DURING THE PROJECT.
 10. NO DEVIATIONS TO THE PLANS SHALL TAKE PLACE UNLESS PRIOR APPROVAL FROM THE OWNER, PROJECT ENGINEER, AND THE APPROPRIATE REVIEW AGENCIES.

E&SC MEASURES

3.02	TEMPORARY STONE CONSTRUCTION ENTRANCE	CE
3.05	SILT FENCE	SF
3.07	STORM DRAIN INLET PROTECTION	IP
3.09	TEMPORARY DIVERSION DIKE	DD
3.13	TEMPORARY SEDIMENT TRAP	ST
3.18	OUTLET PROTECTION	OP
3.31	TEMPORARY SEEDING	TS
3.32	PERMANENT SEEDING	PS
3.35	MULCHING	MU
3.36	SOIL STABILIZATION BLANKETS & MATTING	B/M

City of Roanoke
Planning, Building, & Development
COMPREHENSIVE DEVELOPMENT PLAN
APPROVED
by Aaron Cypher 03/30/2021

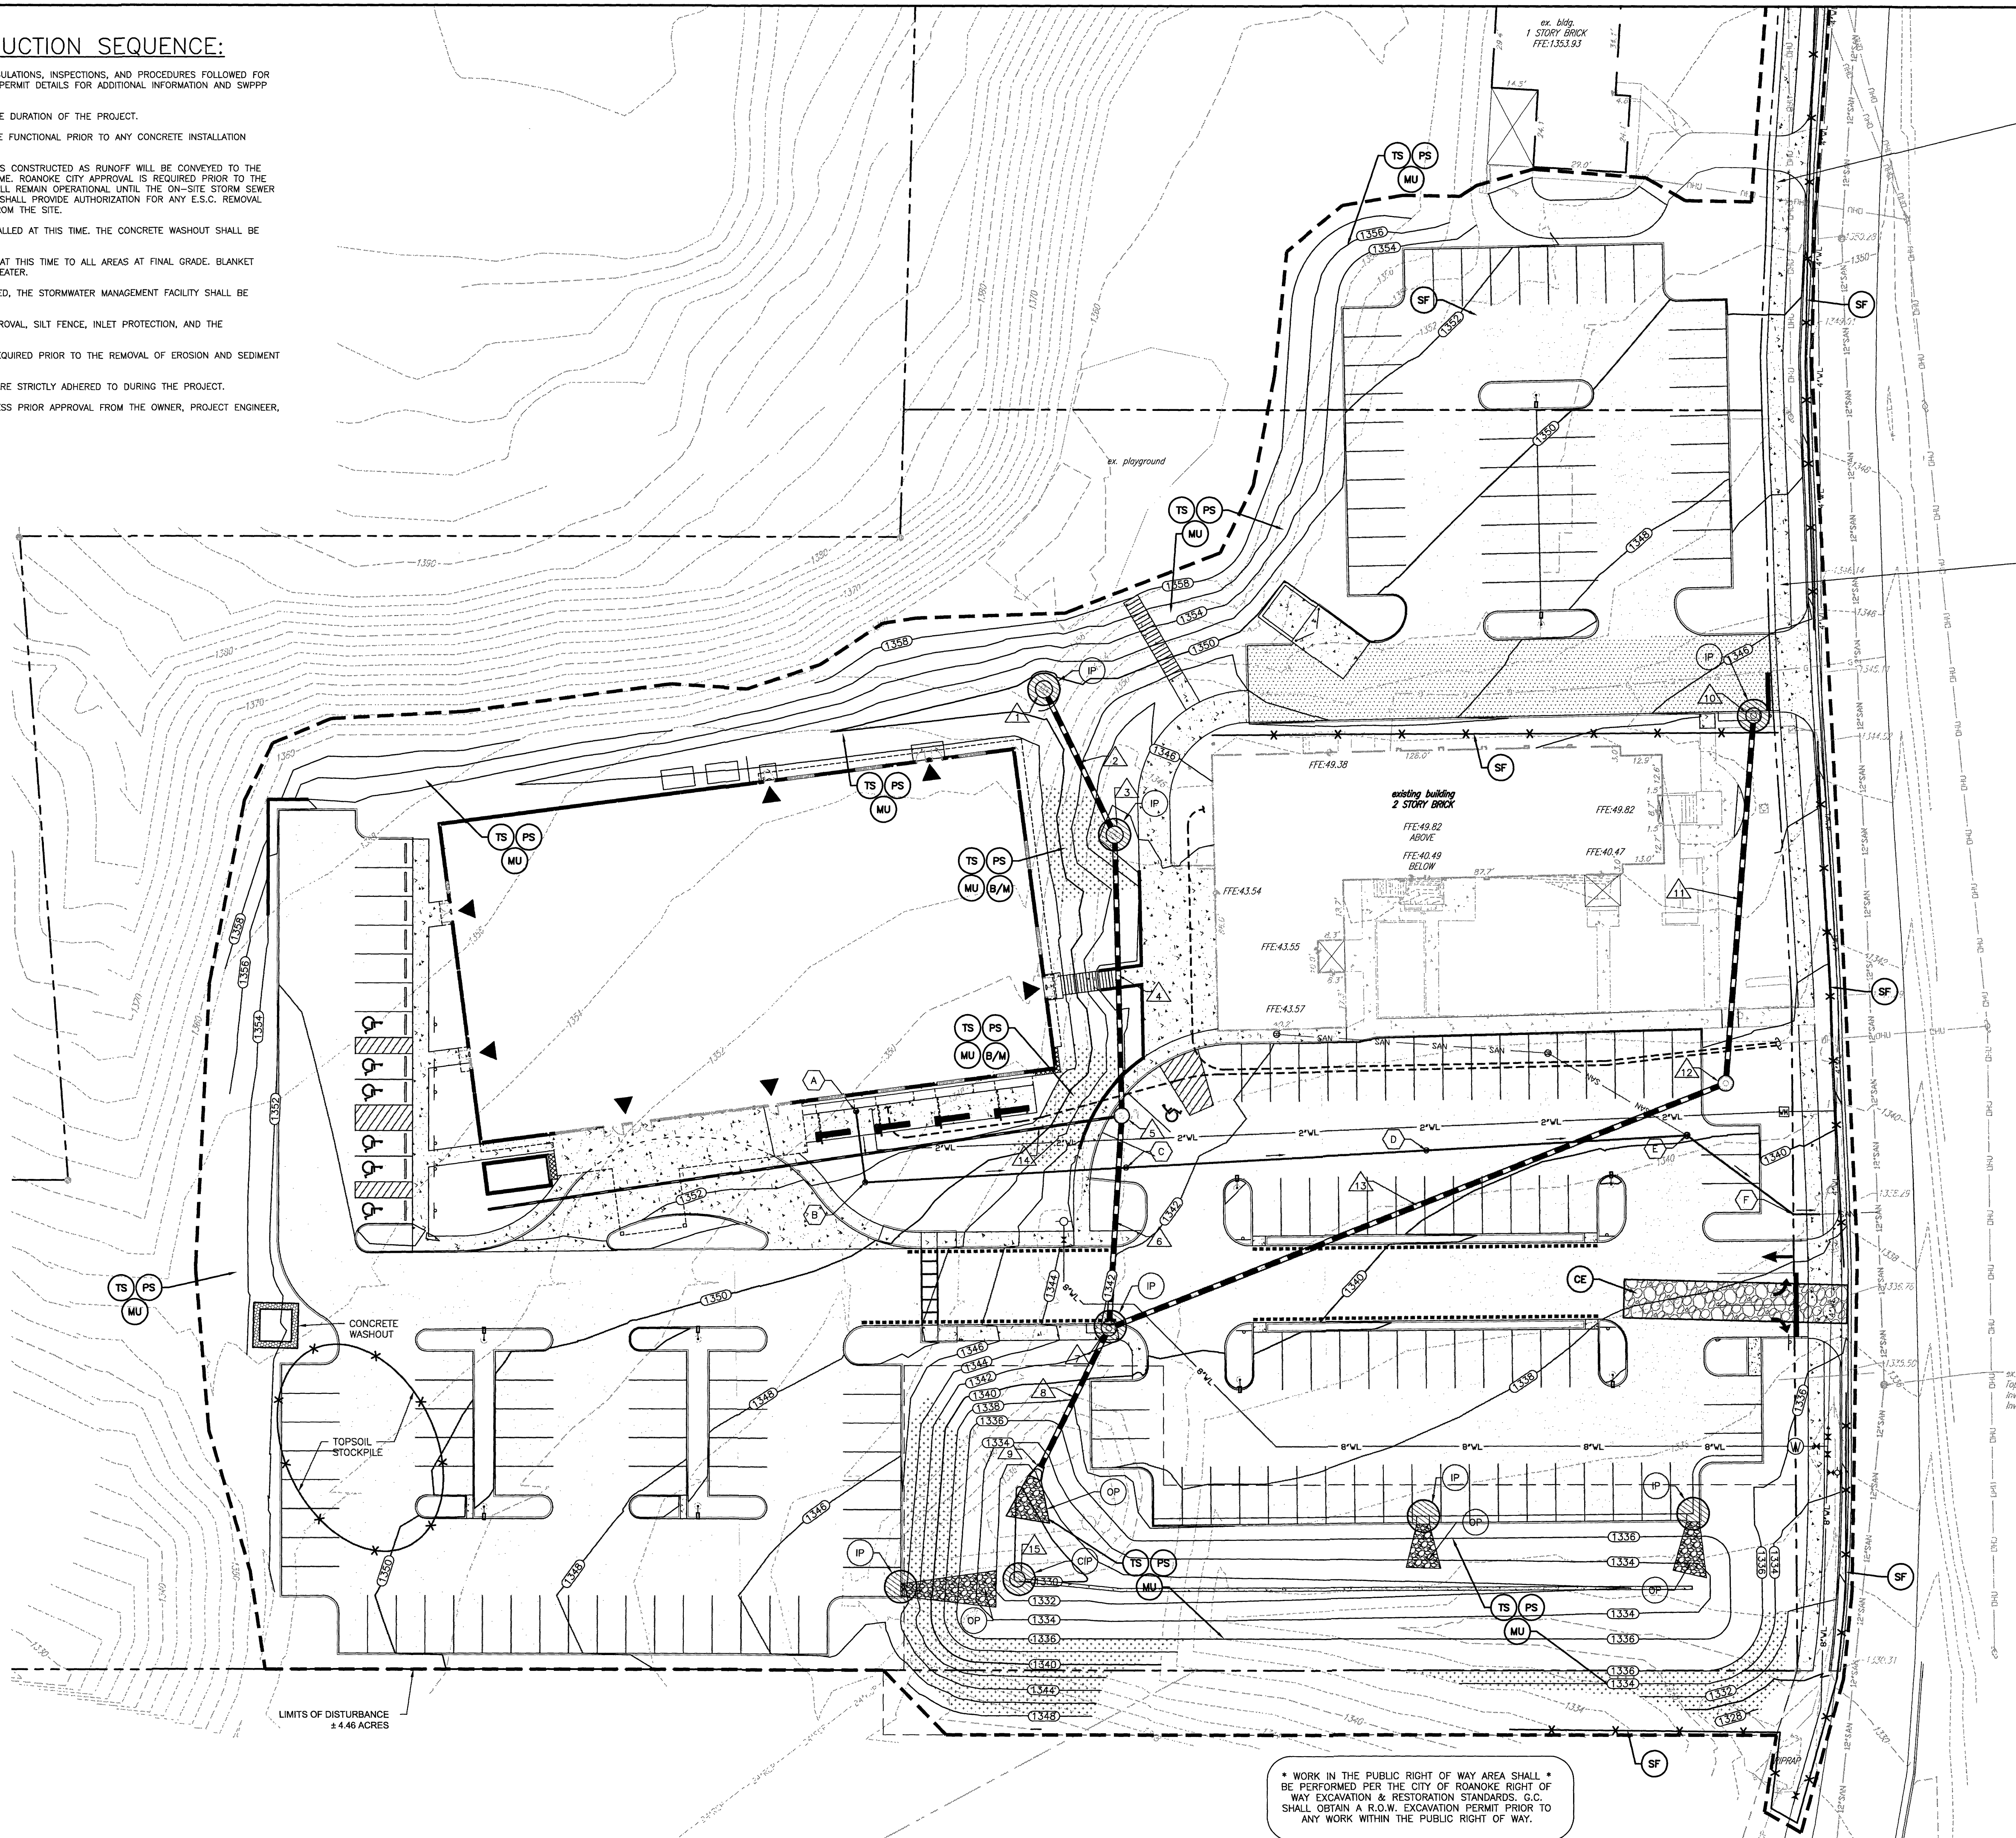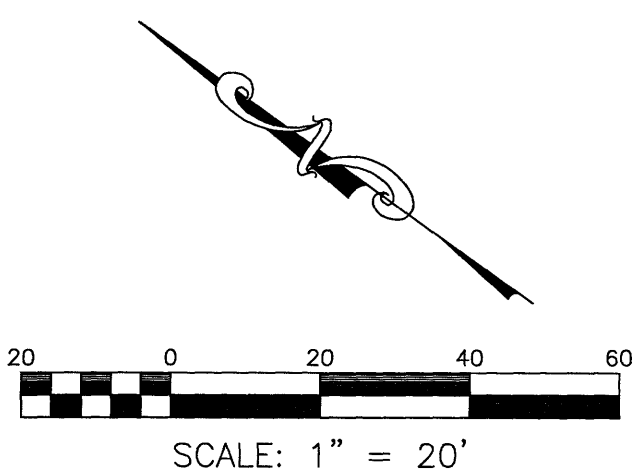


* WORK IN THE PUBLIC RIGHT OF WAY AREA SHALL *
BE PERFORMED PER THE CITY OF ROANOKE RIGHT OF
WAY EXCAVATION & RESTORATION STANDARDS. G.C.
SHALL OBTAIN A R.O.W. EXCAVATION PERMIT PRIOR TO
ANY WORK WITHIN THE PUBLIC RIGHT OF WAY.



**BALZER
& ASSOCIATES**
PLANNERS / ARCHITECTS
ENGINEERS / SURVEYORS

Roanoke / Richmond
New River Valley / Staunton
Harrisonburg / Lynchburg
www.balzer.cc

1208 Corporate Circle
Roanoke, VA 24018
540.772.9580



NEW HOPE CHRISTIAN CHURCH

4229 WELCOME VALLEY RD SE

E.S.C. PLAN - PHASE II

CITY OF ROANOKE, VIRGINIA

DRAWN BY
DESIGNED BY
CHECKED BY
DATE
SCALE
REVISIONS
1/6/2021
1/29/2021

KAM
BTC
BTC
11/17/2020
1" = 20'

C10
PROJECT NO. 04200027.00
