
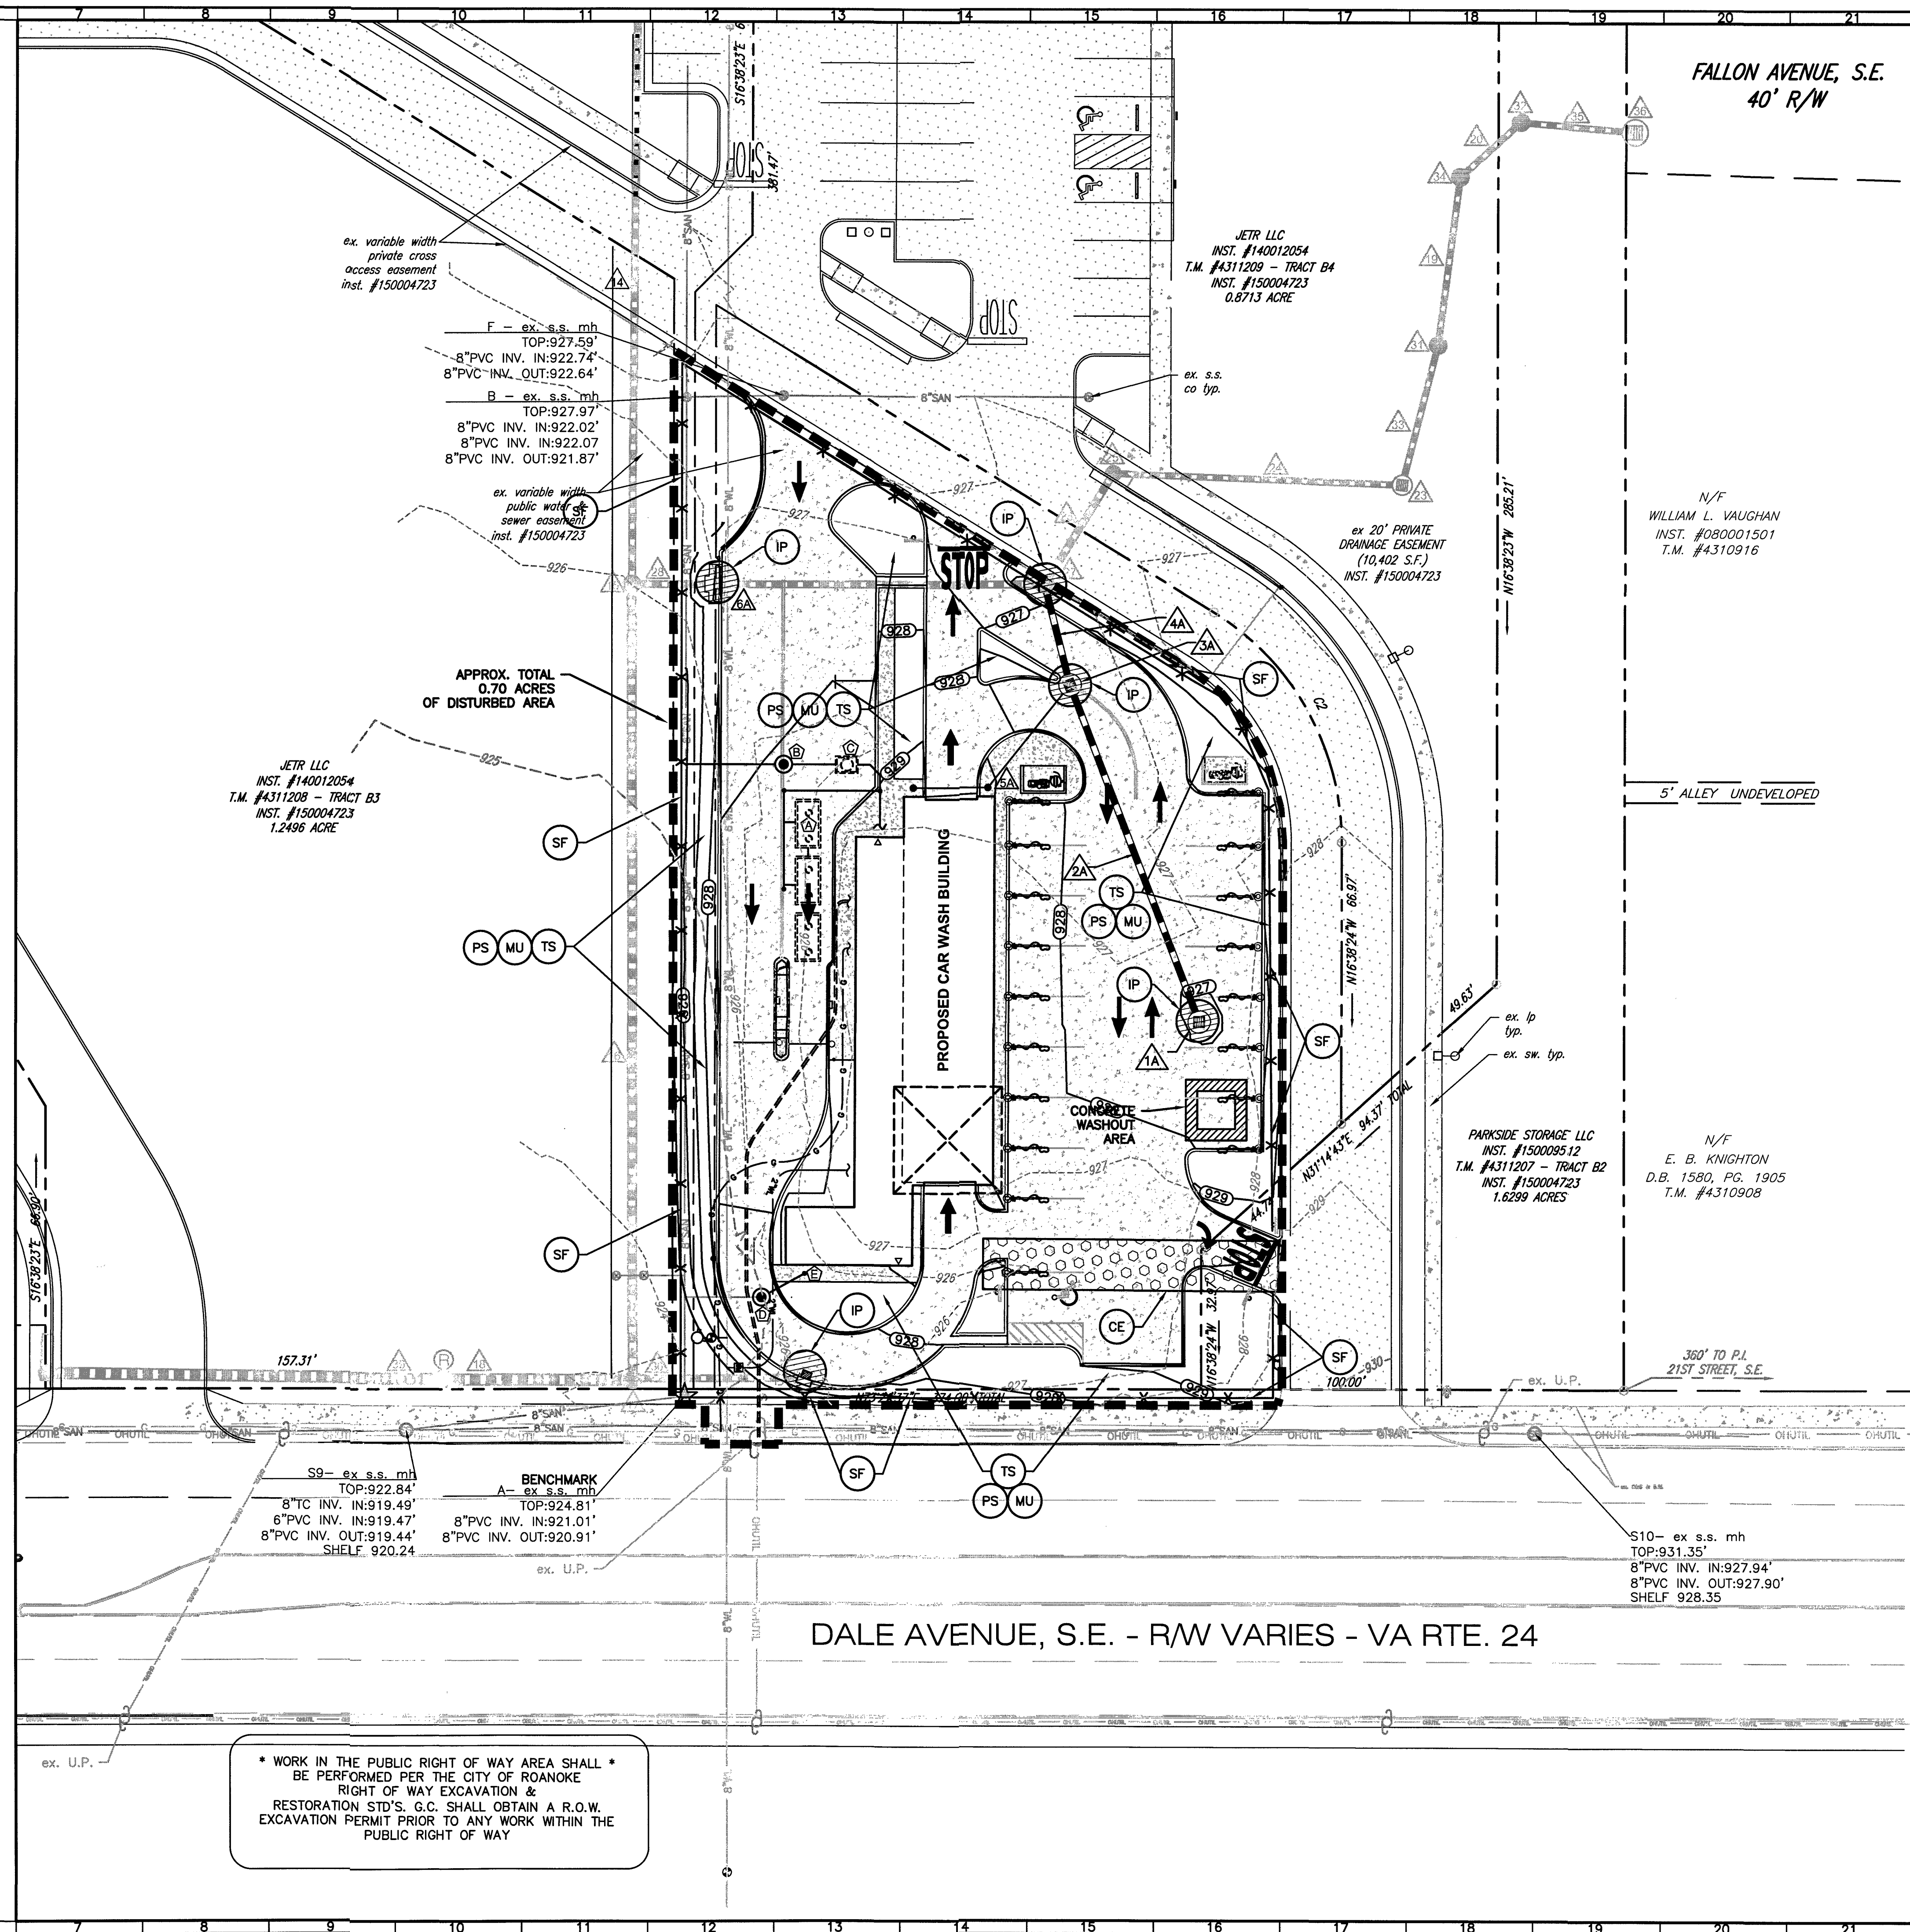


3. THE CONSTRUCTION ENTRANCE SHALL BE INSTALLED AS A FIRST STEP IN THE PROCESS. THE CONSTRUCTION ENTRANCE SHALL BE MAINTAINED WHERE SHOWN UNTIL SUCH TIME THAT THE CONSTRUCTION ENTRANCE IS NO LONGER NEEDED AND THE EXISTING STONE BASE OR ASPHALT PAVING/CONCRETE ENTRANCE HAS BEEN INSTALLED. THE CONSTRUCTION ENTRANCE SHALL REMAIN IN PLACE UNTIL SUCH TIME THAT THE INSPECTOR APPROVES ITS REMOVAL.
4. SILT FENCE AND ANY PERIMETER CONSTRUCTION FENCING SHALL BE INSTALLED AT THIS TIME TO PREVENT SEDIMENT LADEN RUNOFF FROM EXITING THE SITE. THE SILT FENCE SHALL BE MAINTAINED THROUGHOUT THE DURATION OF THE PROJECT PER THE VA ESC HANDBOOK.
5. G.C. SHALL TAKE APPROPRIATE MEASURES TO MINIMIZE 'MUD TRACKING' ON THE ADJACENT PUBLIC RIGHT OF WAY. GRADING OPERATIONS SHALL TAKE PLACE AT THIS TIME ON-SITE.
6. G.C. SHALL UTILIZE A CONCRETE WASHOUT AREA AS REQUIRED FOR THE PROJECT ONCE CONSTRUCTION PROGRESSES TO BUILDING OR SITE CONCRETE INSTALLATION.
7. STORM SEWER SHALL BE INSTALLED AT THIS TIME AND ALL INLETS SHALL BE SEDIMENT PROTECTED AS REQUIRED.
8. INSTALL SANITARY SEWER AND WATERLINE IMPROVEMENTS AS SHOWN ON THE PLAN AND PROVIDE DEWATERING AS REQUIRED FOR CONSTRUCTION.
9. ALL OTHER SITE UTILITIES SHALL BE INSTALLED AT THIS TIME INCLUDING ELECTRICAL, LIGHTING, GAS, CONDUIT, ETC.
10. CURB, STREET TREES, SIDEWALK, AND LANDSCAPING SHALL BE INSTALLED AT THIS TIME.
11. PERMANENT SEEDING OR MULCHING SHALL BE APPLIED TO ALL LANDSCAPE AREAS AND AREAS NOT RECEIVING HARDCAPE ELEMENTS.
12. AFTER STABILIZATION OF ALL UPSTREAM AREAS, INLET PROTECTION AND SILT FENCE MAY BE REMOVED WITH CITY OF ROANOKE INSPECTOR APPROVAL.
13. CITY OF ROANOKE SHALL INSPECT/APPROVE REMOVAL OF REQUIRED MEASURES PRIOR TO ESC MEASURE REMOVAL.

3.02	TEMPORARY STONE CONSTRUCTION ENTRANCE	CE
3.05	SILT FENCE	SF
3.07	STORM DRAIN INLET PROTECTION	IP
3.31	TEMPORARY SEEDING	TS
3.32	PERMANENT SEEDING	PS
3.35	MULCHING	MU
	CONCRETE WASHOUT	CWO



SHEET NO.

C5

JOB NO. 04150069.00
