


J:\2020\04\02\2008.00 - SOUTHERN TEAM HYUNDAI\0422008.00 Final Review 2 2023-04-18.dwg PLOTTED: 10/30/2023 7:28:23 AM

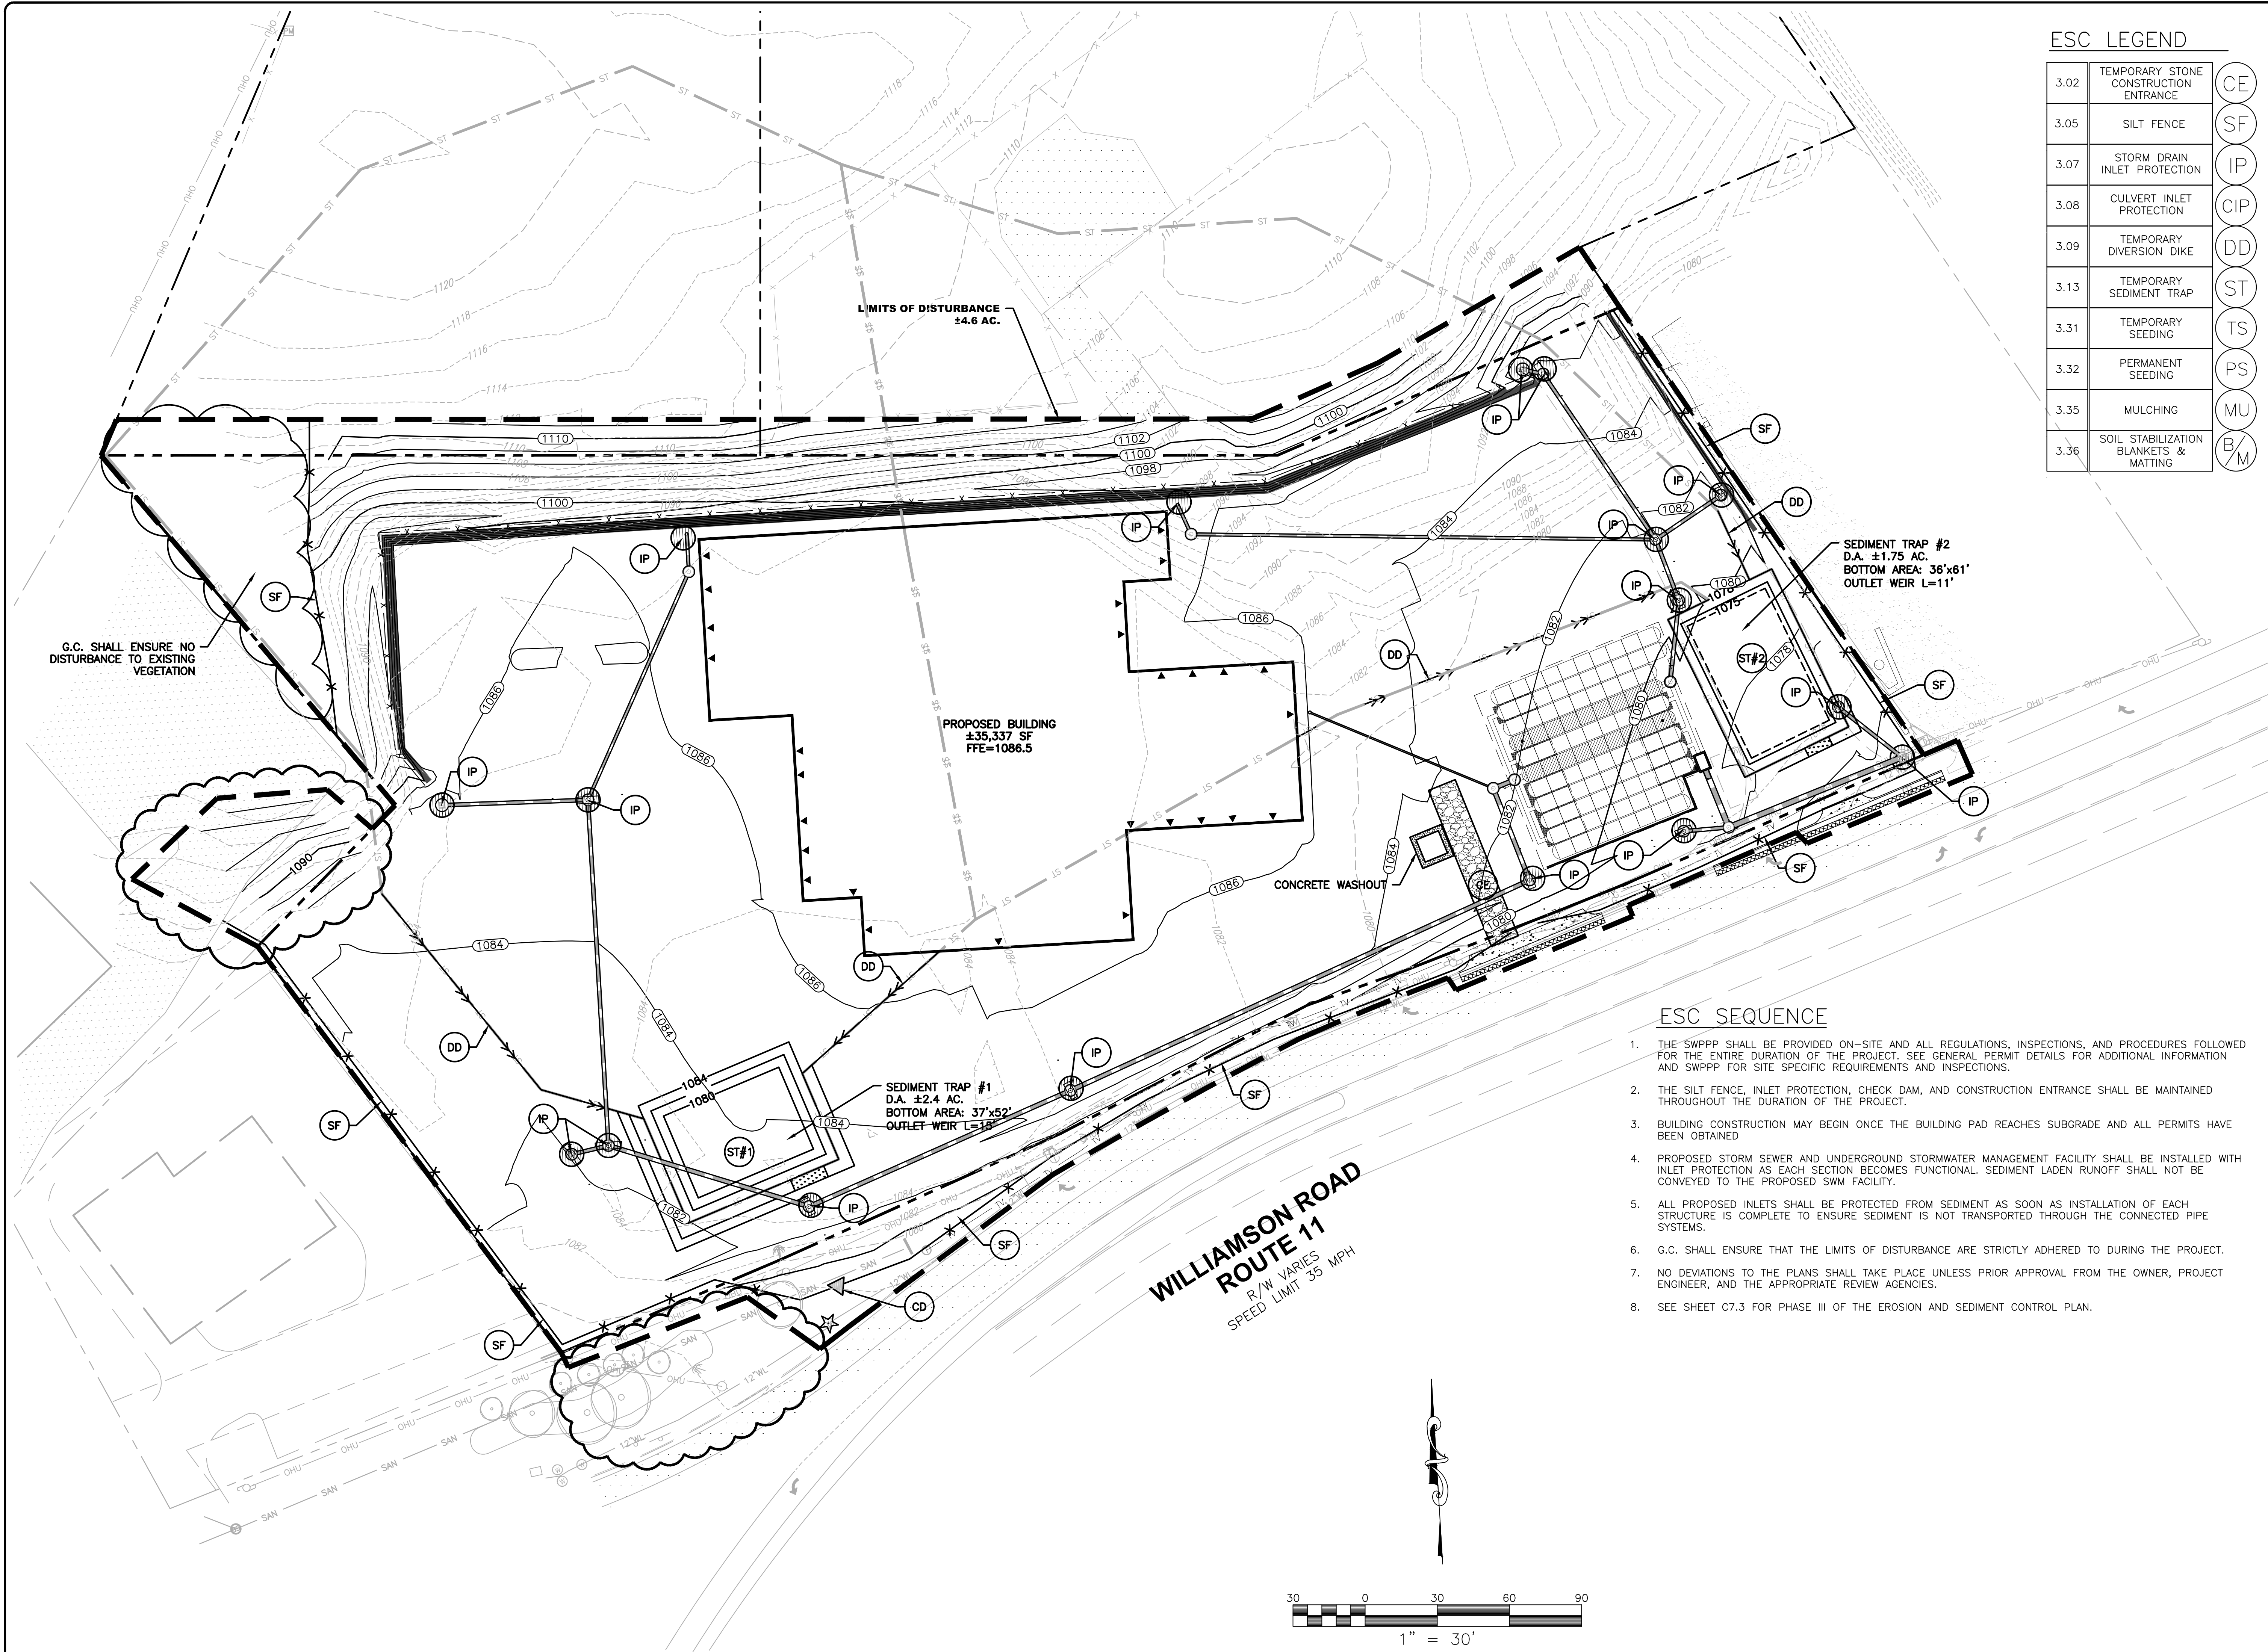

ESC LEGEND		
3.02	TEMPORARY STONE CONSTRUCTION ENTRANCE	CE
3.05	SILT FENCE	SF
3.07	STORM DRAIN INLET PROTECTION	IP
3.08	CULVERT INLET PROTECTION	CIP
3.09	TEMPORARY DIVERSION DIKE	DD
3.13	TEMPORARY SEDIMENT TRAP	ST
3.31	TEMPORARY SEEDING	TS
3.32	PERMANENT SEEDING	PS
3.35	MULCHING	MU
3.36	SOIL STABILIZATION BLANKETS & MATTING	B/M


ESC SEQUENCE

1. THE SWPPP SHALL BE PROVIDED ON-SITE AND ALL REGULATIONS, INSPECTIONS, AND PROCEDURES FOLLOWED FOR THE ENTIRE DURATION OF THE PROJECT. SEE GENERAL PERMIT DETAILS FOR ADDITIONAL INFORMATION AND SWPPP FOR SITE SPECIFIC REQUIREMENTS AND INSPECTIONS.
2. THE SILT FENCE, INLET PROTECTION, CHECK DAM, AND CONSTRUCTION ENTRANCE SHALL BE MAINTAINED THROUGHOUT THE DURATION OF THE PROJECT.
3. BUILDING CONSTRUCTION MAY BEGIN ONCE THE BUILDING PAD REACHES SUBGRADE AND ALL PERMITS HAVE BEEN OBTAINED
4. PROPOSED STORM SEWER AND UNDERGROUND STORMWATER MANAGEMENT FACILITY SHALL BE INSTALLED WITH INLET PROTECTION AS EACH SECTION BECOMES FUNCTIONAL. SEDIMENT LADEN RUNOFF SHALL NOT BE CONVEYED TO THE PROPOSED SWM FACILITY.
5. ALL PROPOSED INLETS SHALL BE PROTECTED FROM SEDIMENT AS SOON AS INSTALLATION OF EACH STRUCTURE IS COMPLETE TO ENSURE SEDIMENT IS NOT TRANSPORTED THROUGH THE CONNECTED PIPE SYSTEMS.
6. G.C. SHALL ENSURE THAT THE LIMITS OF DISTURBANCE ARE STRICTLY ADHERED TO DURING THE PROJECT.
7. NO DEVIATIONS TO THE PLANS SHALL TAKE PLACE UNLESS PRIOR APPROVAL FROM THE OWNER, PROJECT ENGINEER, AND THE APPROPRIATE REVIEW AGENCIES.
8. SEE SHEET C7.3 FOR PHASE III OF THE EROSION AND SEDIMENT CONTROL PLAN.



BALZER & ASSOCIATES
PLANNERS / ARCHITECTS
ENGINEERS / SURVEYORS

Roanoke / Richmond
Shenandoah Valley
New River Valley / Lynchburg
www.balzer.cc
1208 Corporate Circle
Roanoke, VA 24018
540.772.9580



SOUTHERN TEAM HYUNDAI

ESC PLAN PHASE II

DRAWN BY KAM
DESIGNED BY BTC
CHECKED BY BTC
DATE 5/16/2022
SCALE 1" = 30'
REVISIONS
7/15/2022
8/10/2022
2/23/2023 PR#1
7/10/2023 PR#2
10/3/2023 PR#3

C7.2
PROJECT NO. 0422008.00
