



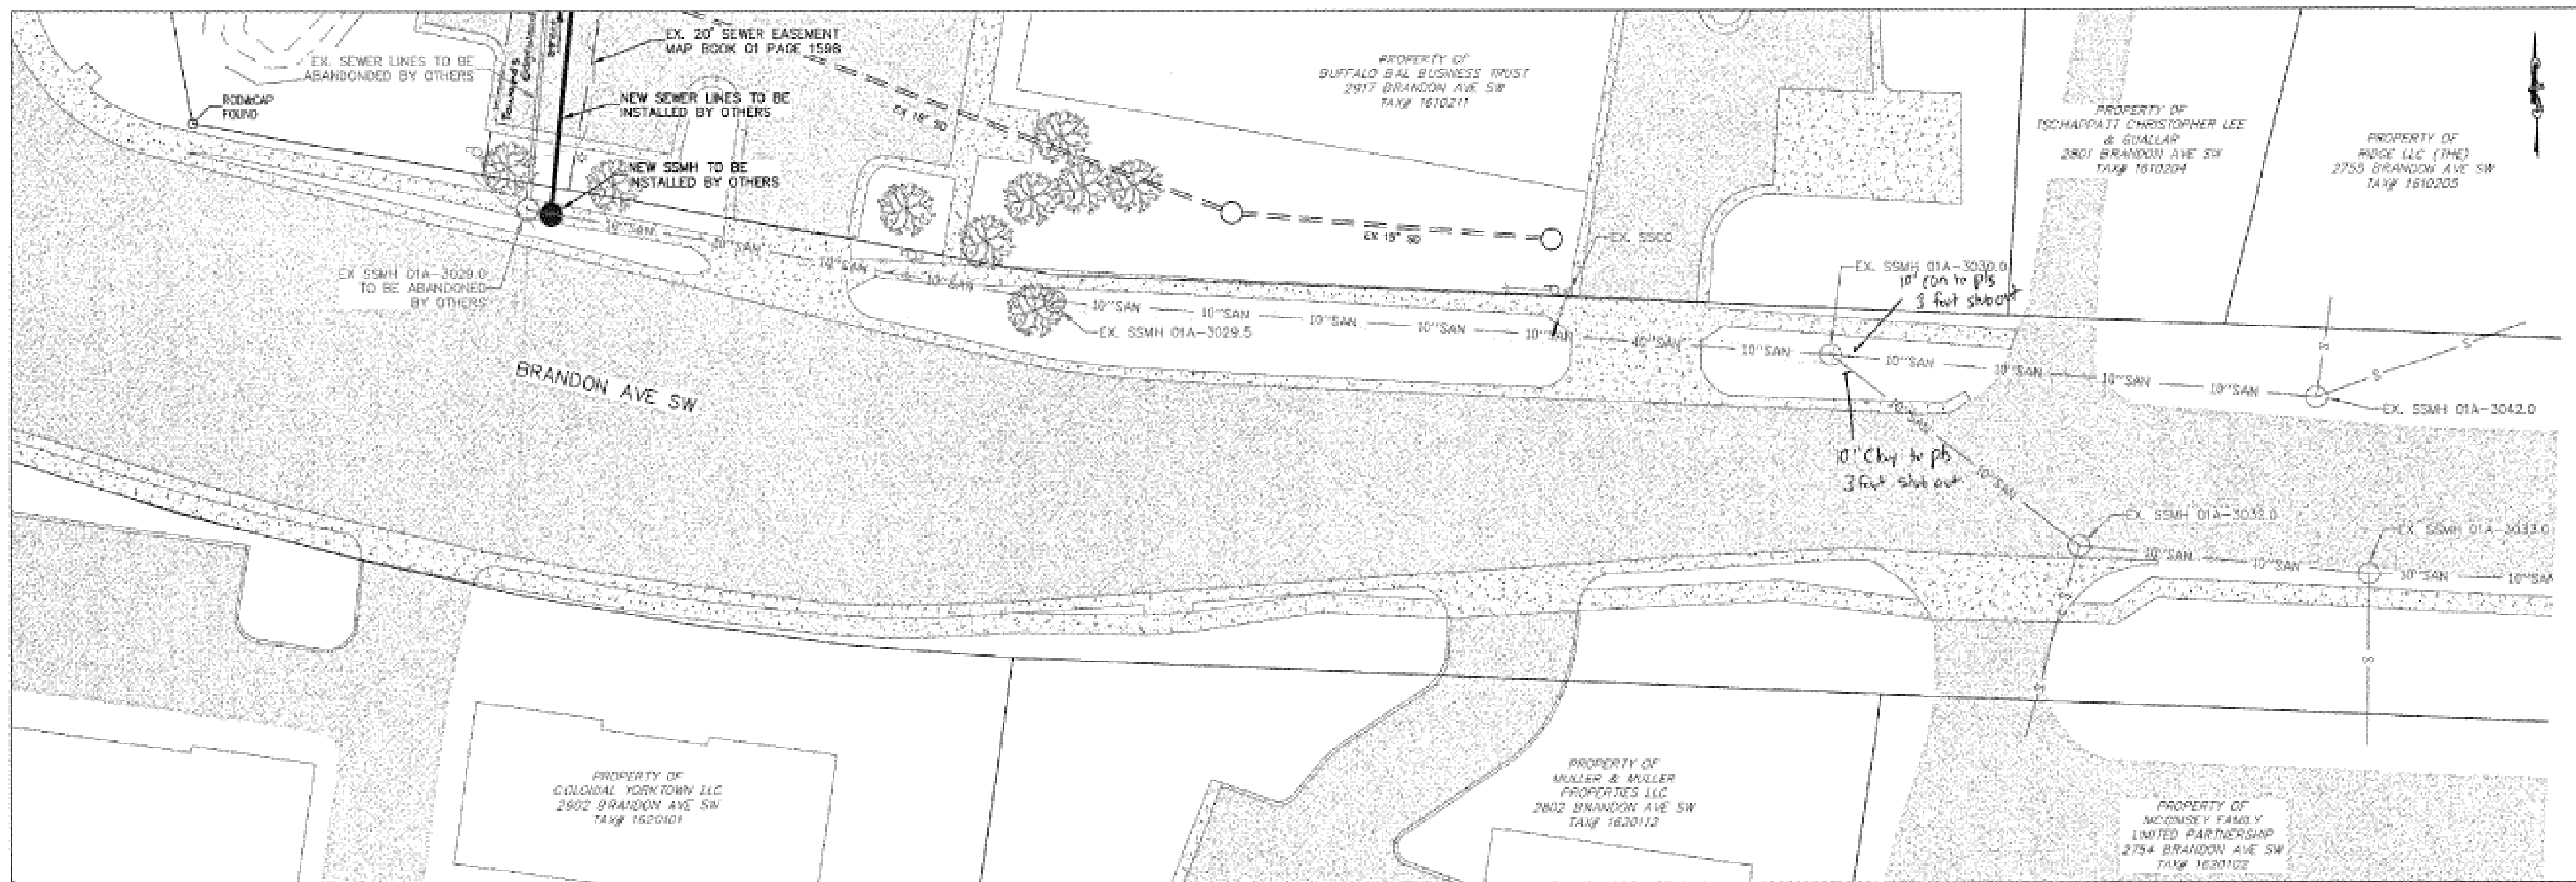

Project Name	Brandon Ave Sewer
Contractor	Joseph Rowan CIP3
Construction Start Date	1/11/21
Completion Date	1/29/21
Sewer Gravity Main(s)	
Manufacturer	
Diameter	12"
Pipe Class	DR 17
Material	Plastic fusion
Comments	
Sewer Gravity Lateral(s)	
Manufacturer	
Diameter	4"
Pipe Class	Sch 40
Material	Plastic
Comments	
Sewer Manhole(s)	
Manufacturer	CSI
Material	Concrete
Ring & Cover Manuf.	CMC
Cover Type	Water tight
Comments	

- All Green was replaced with 12" DR 17 fusion pipe (Existing 10" clay sewer main was pipebursted)
- New 4" connection sch 40 pipe

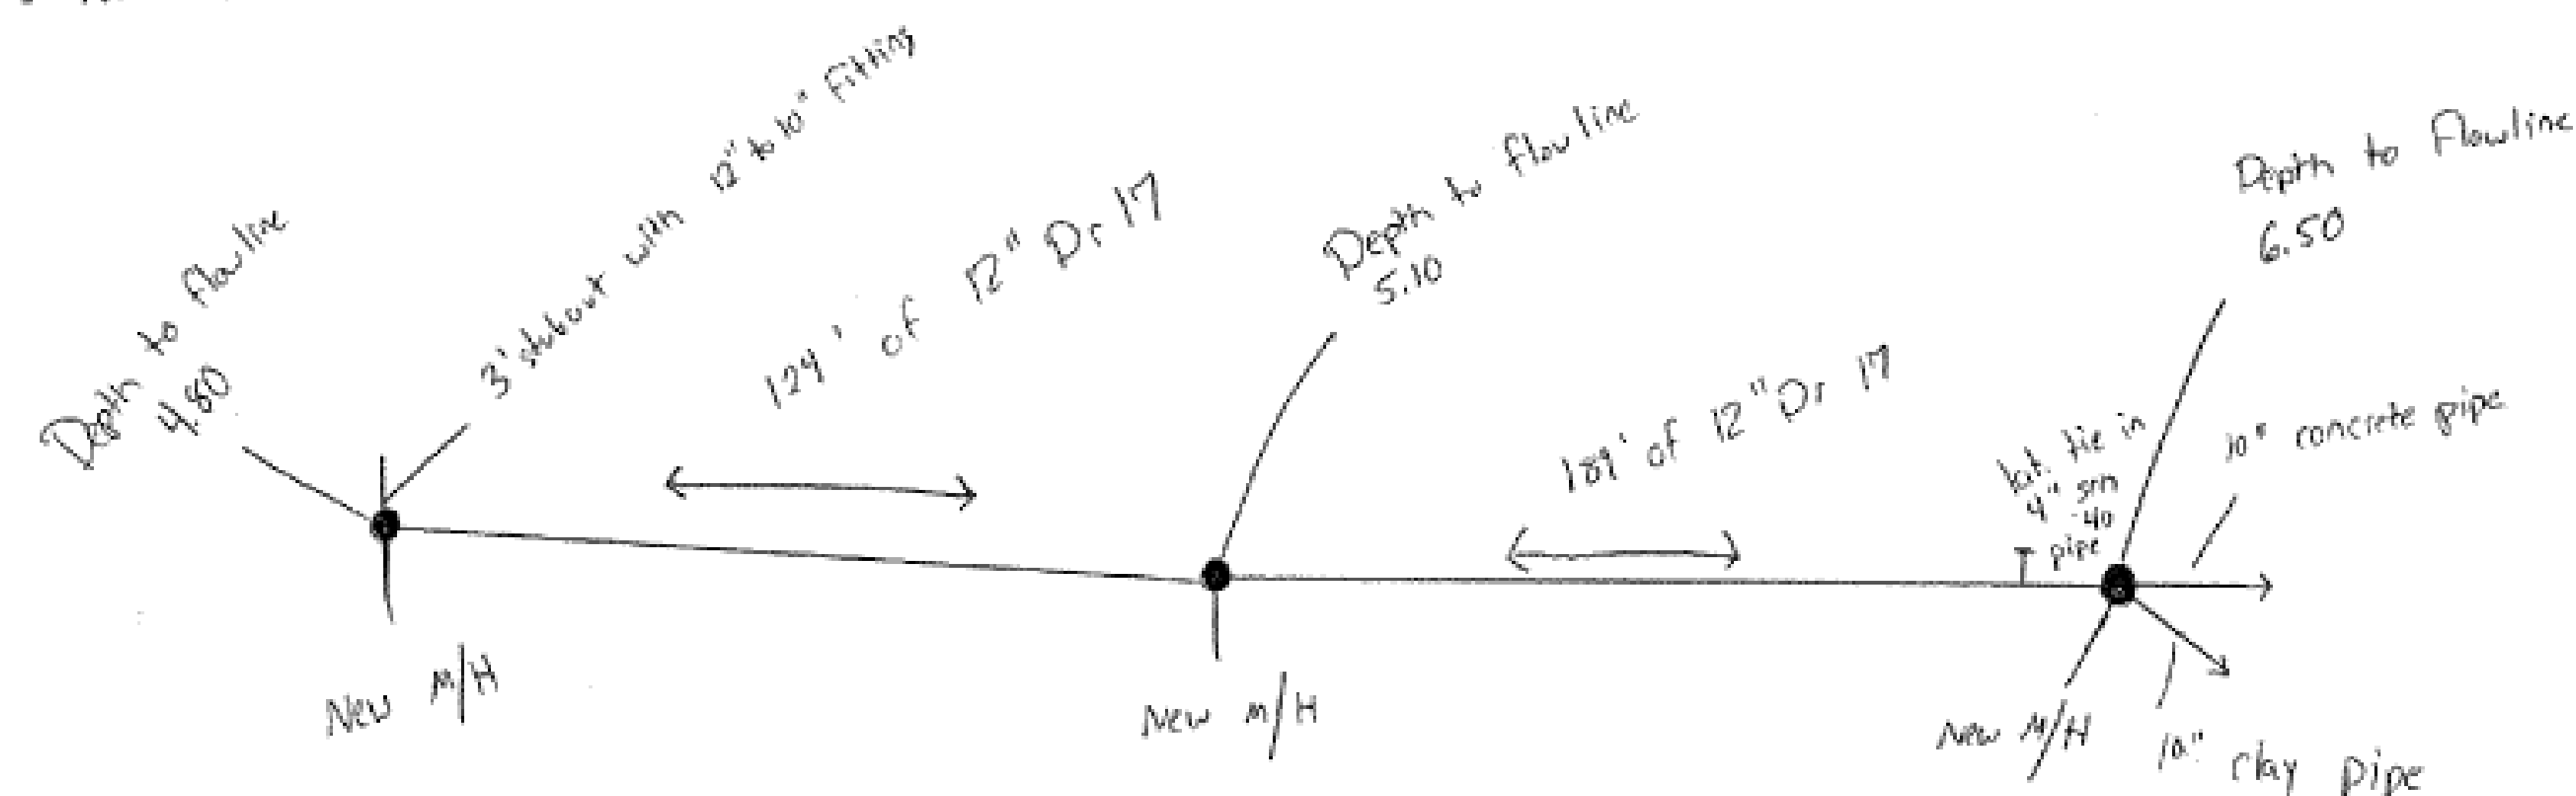

- GENERAL NOTES:
- SEWER LATERALS SHOWN ARE BASED ON CCTV FOOTAGE. ADDITIONAL LATERALS & CONFLICTS SHALL BE INVESTIGATED BY CONTRACTOR PRIOR TO EXCAVATION.
 - PROPERTY LINES SHOWN ON THIS PAGE WERE SET BASED ON RECORDS AND FIELD SURVEY DATA.

Rev	Description	Date	By

Designed:
 Drawn: NSS, AJC
 Checked: DRJ
 Approved:
 Date: JAN 2021
 Project: SCIP-304
