


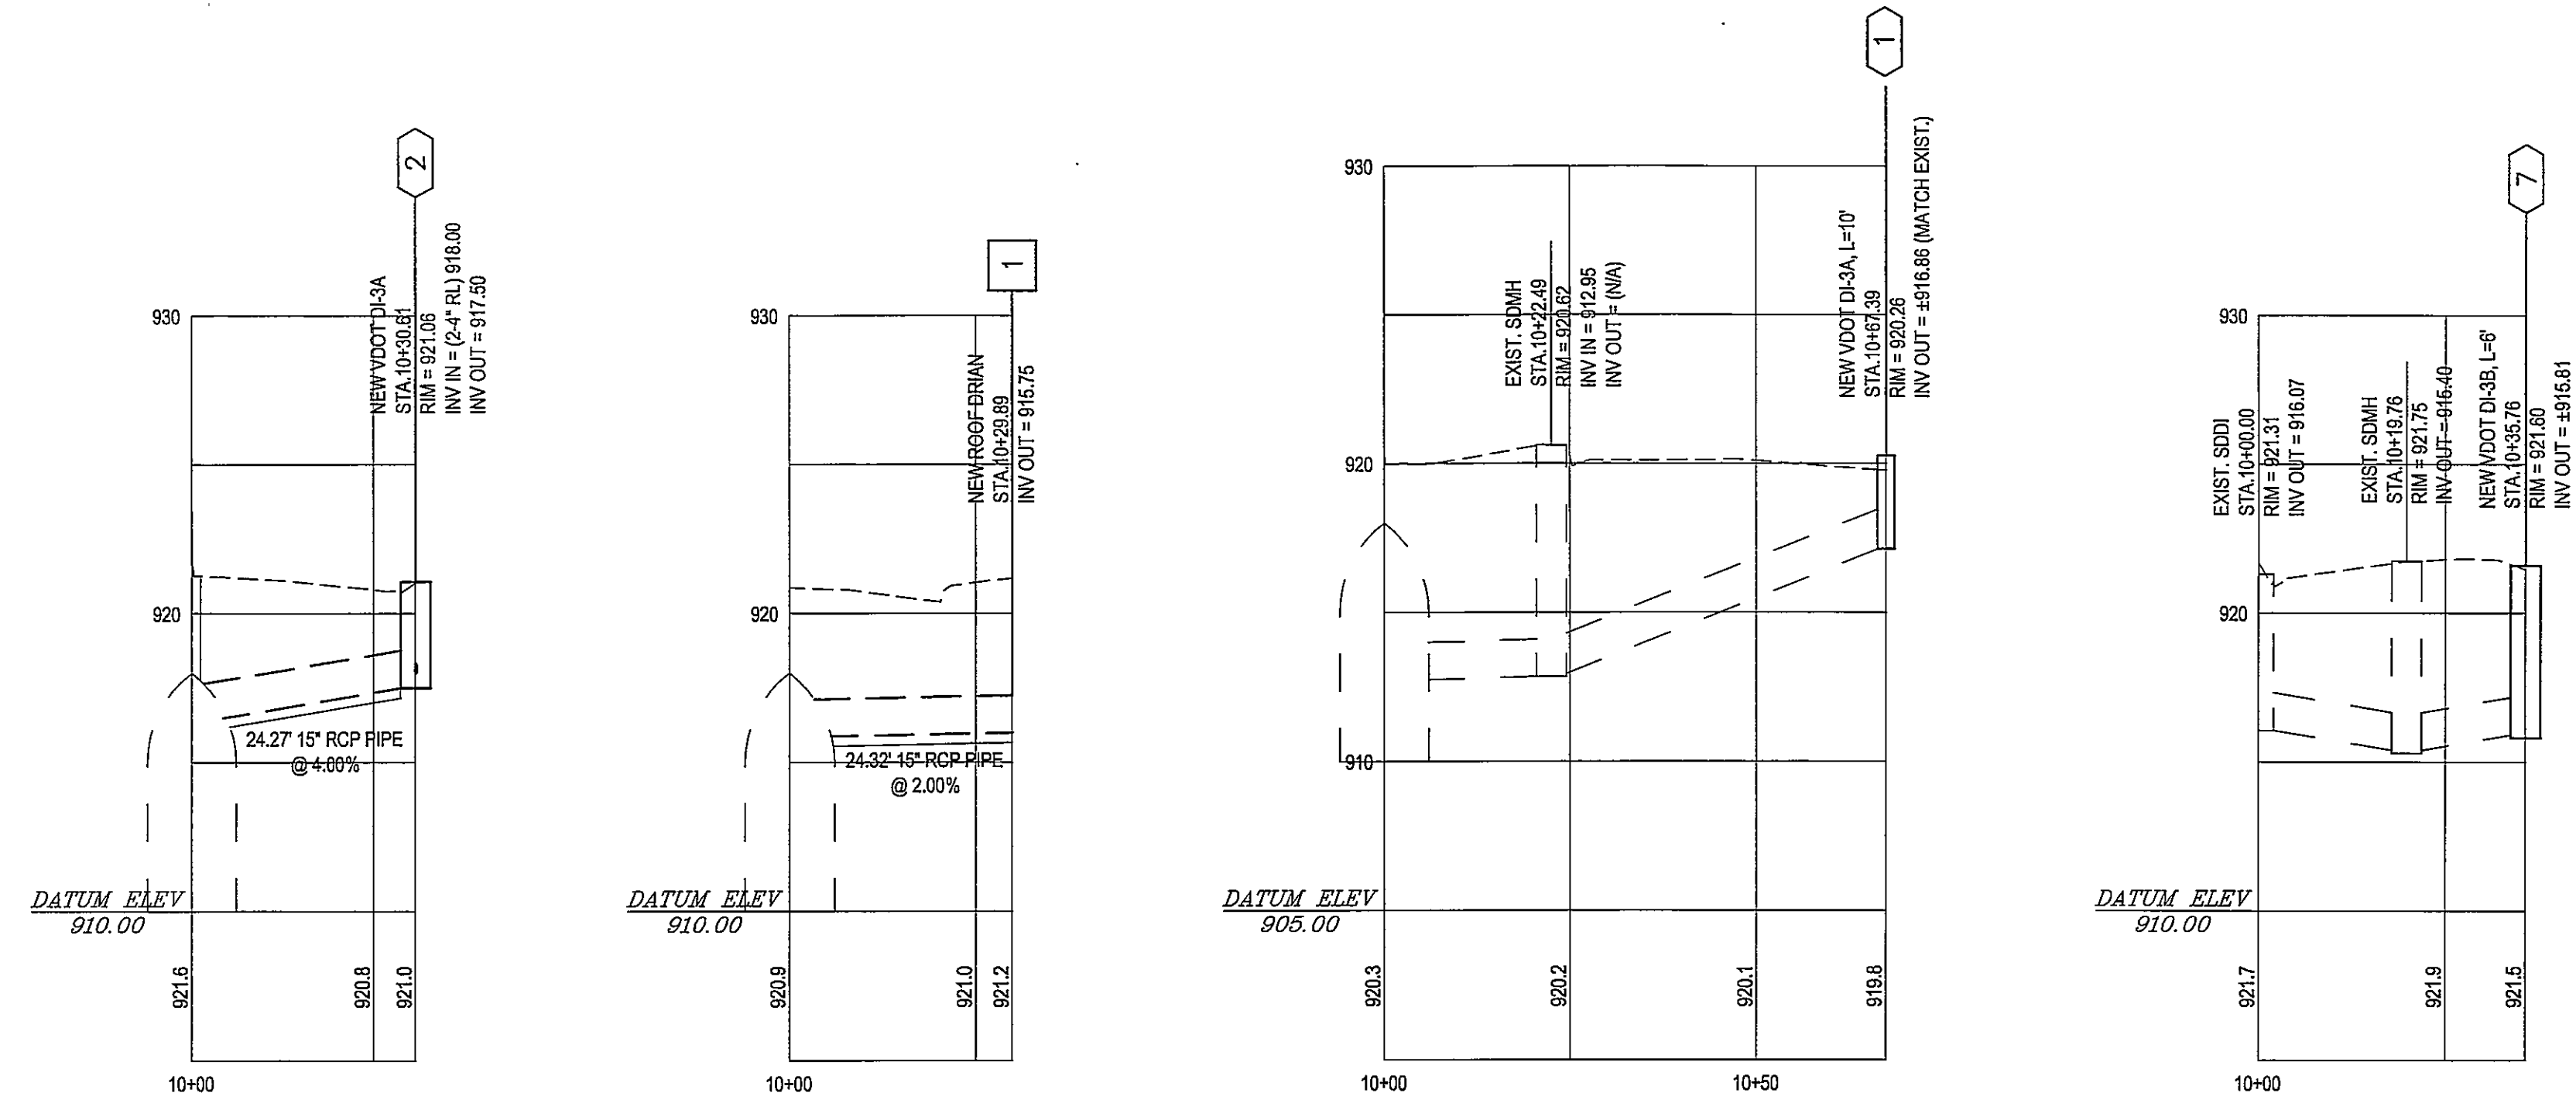

STORM DRAIN PROFILES


SCALE: 1"=20' H 1"=5' V

GENERAL NOTES

- THIS EROSION AND SEDIMENT CONTROL (ESC) SHEET SHOWS ESC MEASURES WHICH ARE TO BE CONSTRUCTED DURING VARIOUS PHASES OF THE SITE GRADING AND CONSTRUCTION. NOT ALL ESC MEASURES ARE NECESSARY TO COMPLETE EACH PHASE OF THE WORK SHOWN.
- PERMANENT OR TEMPORARY SOIL STABILIZATION SHALL BE APPLIED TO DENUDED AREAS WITHIN SEVEN (7) DAYS AFTER FINAL GRADE IS REACHED ON ANY PORTION OF THE SITE. TEMPORARY SOIL STABILIZATION SHALL BE APPLIED WITHIN SEVEN (7) DAYS TO DENUDED AREAS THAT MAY NOT BE AT FINAL GRADE BUT WILL REMAIN DORMANT FOR LONGER THAN THIRTY (30) DAYS. PERMANENT STABILIZATION SHALL BE APPLIED TO AREAS THAT ARE TO BE LEFT DORMANT FOR MORE THAN ONE YEAR.
- THE CONTRACTOR SHALL INSTALL AND MAINTAIN ALL EROSION AND SEDIMENT CONTROL MEASURE SHOWN HEREON AND SHALL COMPLY WITH THE "VIRGINIA EROSION AND SEDIMENT CONTROL HANDBOOK", LATEST EDITION.
- IF OFF-SITE FILL OR BORROW AREAS ARE TO BE USED THE LOCATION OF OFF-SITE FILL OR BORROW AREAS WILL BE PROVIDED TO THE CITY OF ROANOKE PLANNING, BUILDING, AND DEVELOPMENT DEPARTMENT. AN EROSION AND SEDIMENT CONTROL PLAN FOR THE FILL/BORROW SITES SHALL BE SUBMITTED AND APPROVED PRIOR TO THE ISSUANCE OF A LAND DISTURBANCE PERMIT.
- PERMANENT SEEDING APPLIED TO ALL MECHANICALLY STABILIZED SLOPES AND SLOPES STEEPER THAN 3:1 SHALL MEET THE FOLLOWING MIXTURE:

POUNDS PER ACRE	SEED TYPE
108	KENTUCKY 31
2	RED TOP
20	SEASONAL NURSE CROP (ANNUAL RYE, FOXHAIL MILLET, & WINTER RYE MIX)
20	CROWN VETCH
- A LAND DISTURBANCE PERMIT WILL NOT BE ISSUED UNTIL AN EROSION AND SEDIMENT CONTROL PLAN FOR THE BORROW/FILL SITE IS APPROVED.

TOTAL DISTURBED AREA = 0.90 ACRES

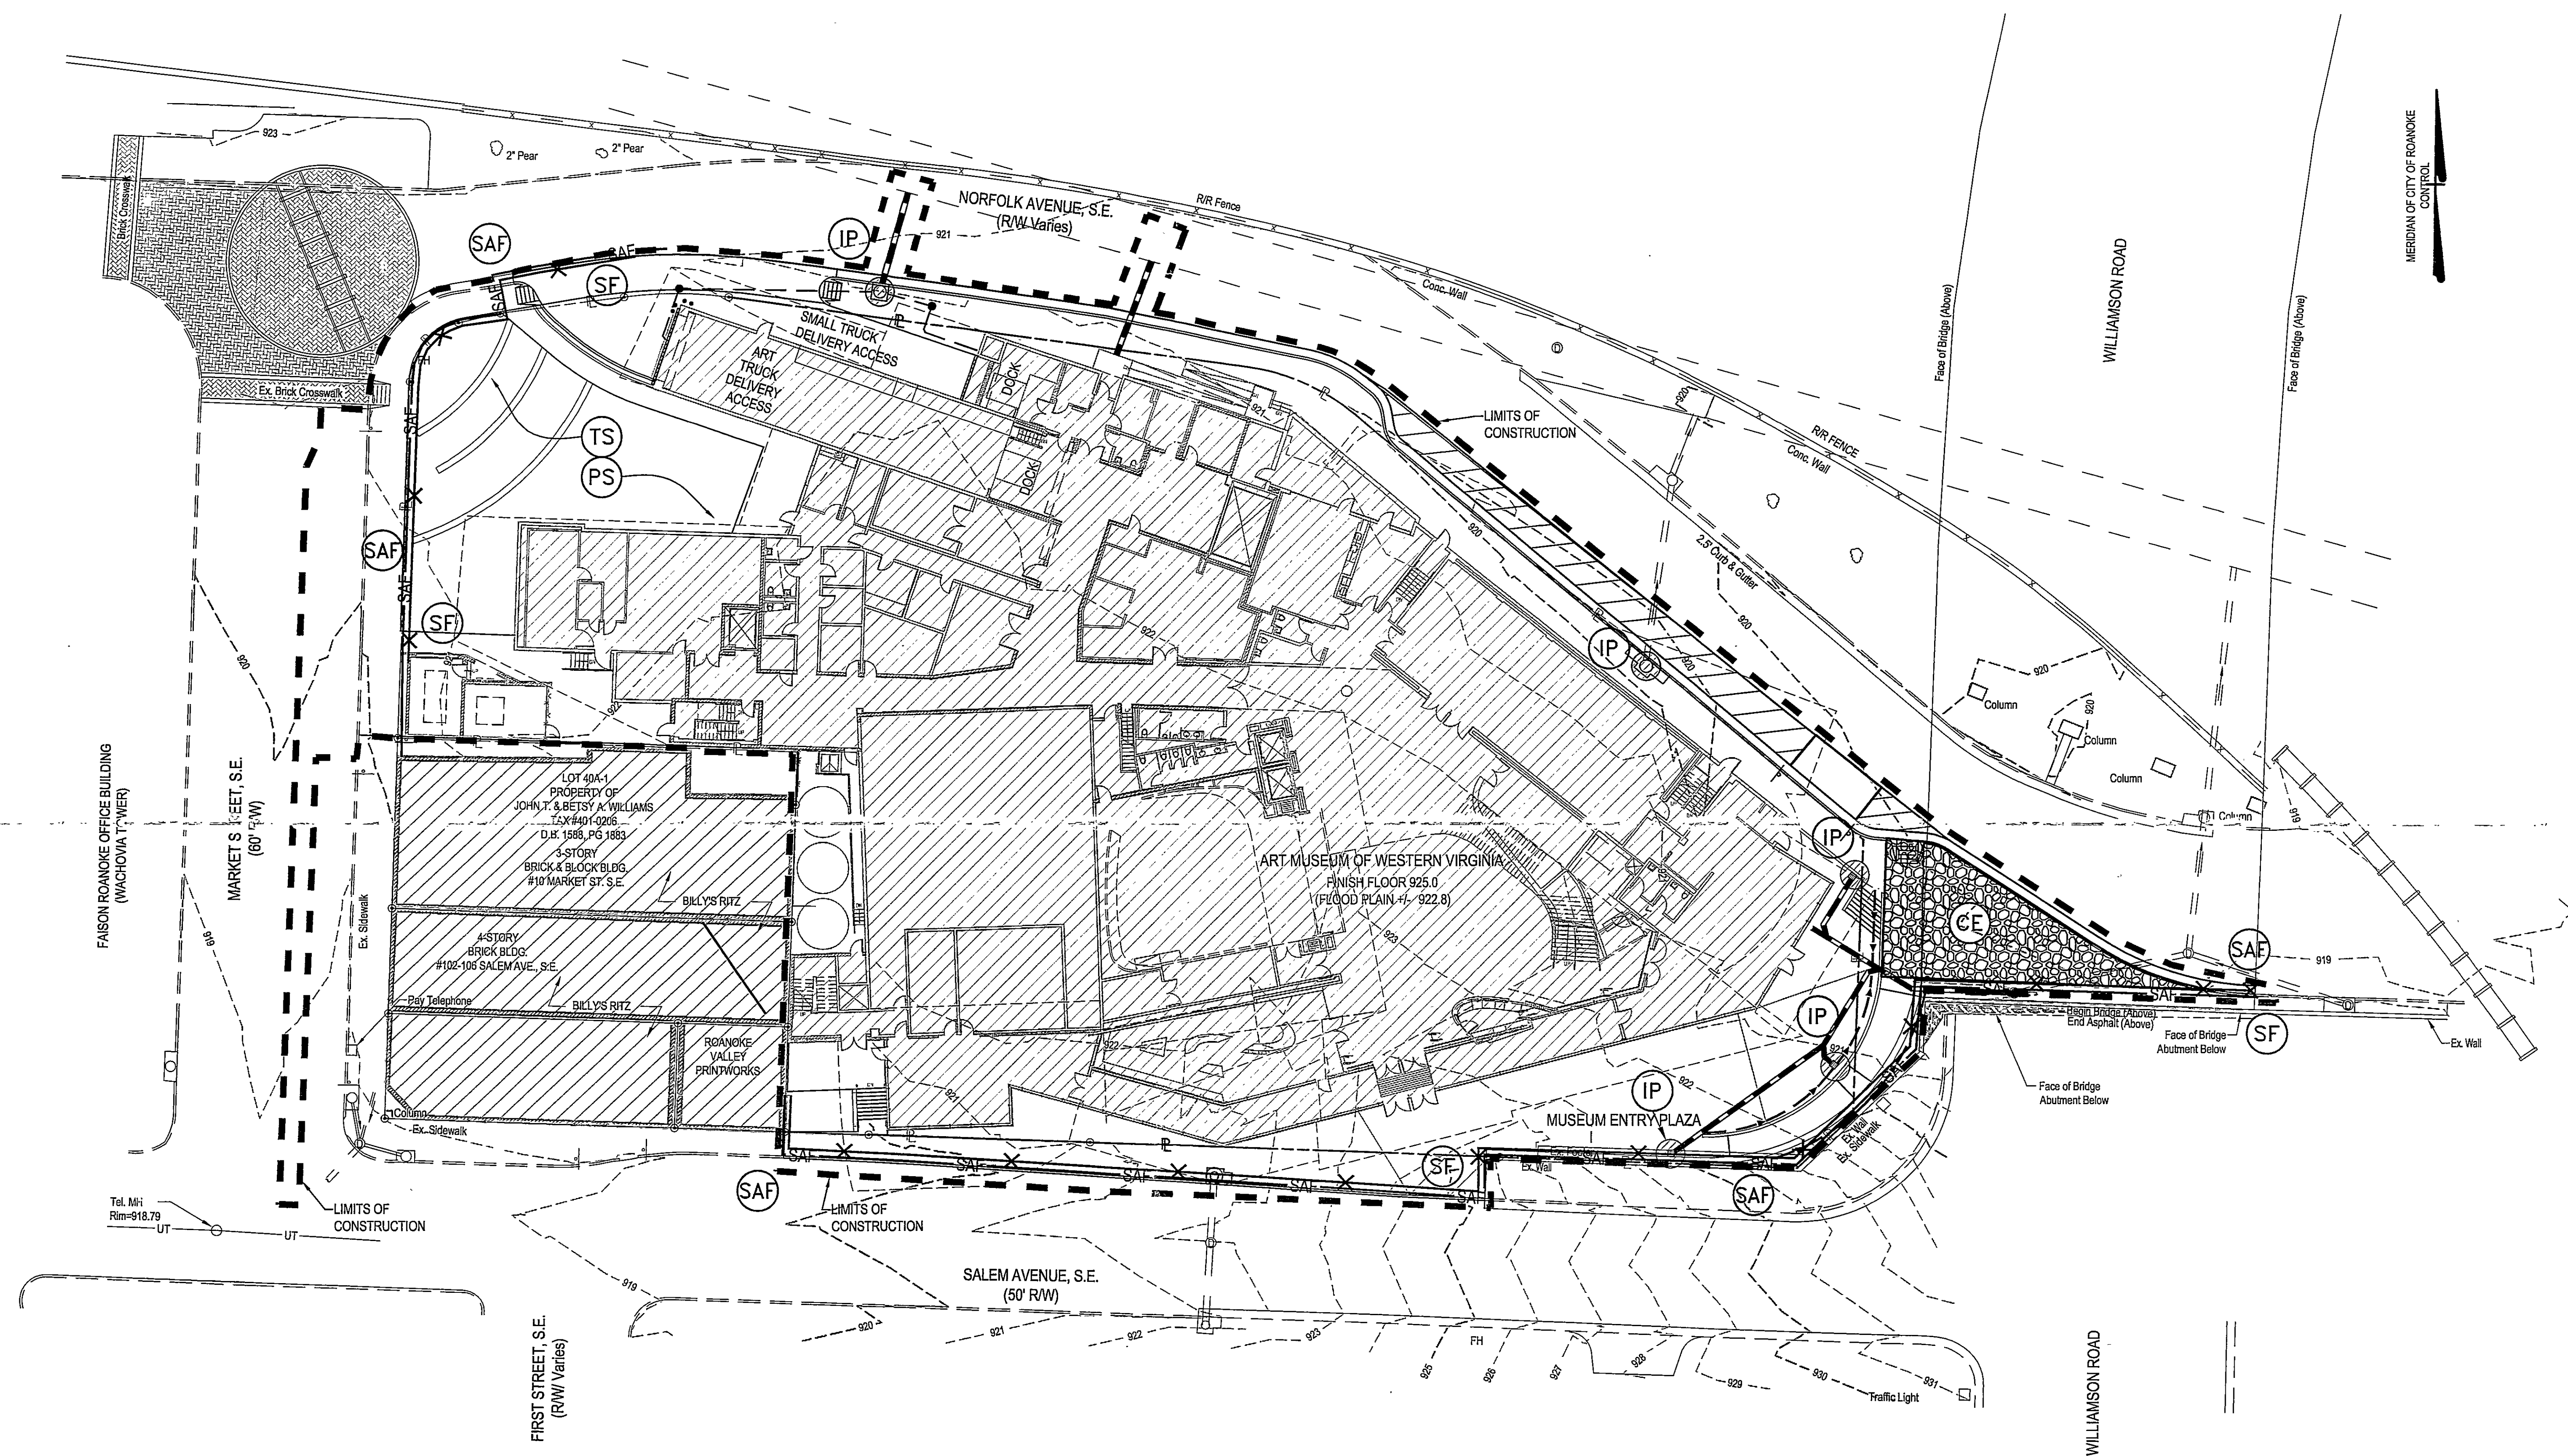

EROSION AND SEDIMENT CONTROL LEGEND

- SAF** SAFETY FENCE (STD. 3.01)
- CE** TEMPORARY STONE CONSTRUCTION ENTRANCE (STD. 3.02)
- SF** SILT FENCE (STD. 3.05)
- IP** INLET PROTECTION (STD. 3.07)
- TS** TEMPORARY SEEDING MIXTURE (STD. 3.31)
- PS** PERMANENT SEEDING MIXTURE (STD. 3.32)
- BM** SOIL STABILIZATION BLANKET/MATTING (STD. 3.36)

SCALE IN FEET
0 20 40

Landscape
Whitesell Group
315 King George Avenue
Roanoke, VA 24016
540.982.0040
gene@whitesellgroup.com

Specifications
Technical Resources Consultants
7180 West Surrey Ave.
Peoria, AZ 85381
623.412.2725
paulsimonsen@trcn.com

Acoustics, AV, Security, Communications
Newcomb & Boyd
303 Peachtree Center Ave. NE, Suite 525
Atlanta, GA 30308-1277
404.730.8400
tferguson@newcomb-boyd.com

Food Service
Webb Design
130 S. Prospect Ave.
Tustin, CA 92780
714.508.1880
jwebb@webbdesignonline.com

Electrical
Kocher, Schirra & Gohariz Consulting Engineers
111 N. Jackson St., Suite 121
Glenside, CA 91038-4317
818.240.5830
hdahl@ksgeng.com

Lighting
LAM Partners
84 Sherman Street
Cambridge, MA 02140
617.354.4502
jennifer@lampartners.com


Structural
Desimone Consulting Engineers PLLC
160 Sansome St., Suite 1600
San Francisco, CA 94104
415.398.5740
drodriguez@de-elmore.com

Mechanical / Plumbing
IBE Consulting Engineers, Inc.
14130 Riverstone Drive, Suite 201
Sherman Oaks, CA 91423
818.377.8220
john.gautrey@ibeco.net

Associate Architect
Rodriguez Ripley Maddux Moley Architects
28 Church Avenue
Roanoke, VA 24011
540.344.1212
guyphk@rmmn.net


Civil
Mattern & Craig
701 First St. S.W.
Roanoke, VA 24016
540.345.9342
w.austin@matternandcraig.com

STAMP



THESE DRAWINGS ARE THE PROPERTY AND COPYRIGHT OF:

randall stout architects, inc.



12894 Washington Blvd.
Los Angeles, CA 90066
310.827.6878 telephone
310.827.6878 facsimile
jmurphy@stoutarc.com

PROJECT

**Art Museum
of
Western Virginia**
100 Salem Avenue SE, Roanoke, Virginia 24011

KEY PLAN

NO.	ISSUE	DATE
1	ADDENDUM #1 (TO 60% DD)	10/25/04
2	100% DD	12/21/04
3	SITE WORK/FOUNDATIONS	07/08/05
4	GMP ISSUE	07/28/05
5	GMP-RU PERMIT APPLICATION	11/18/05

NO.	ISSUE	DATE

DRAWING TITLE

DATE: 08/31/04 DRAWN BY: CZV
PROJECT NO: 0104 REVIEWED BY: WTA
SCALE: SCALE: 1" = 20'

EROSION AND SEDIMENT
CONTROL PLAN

C1-1.25
