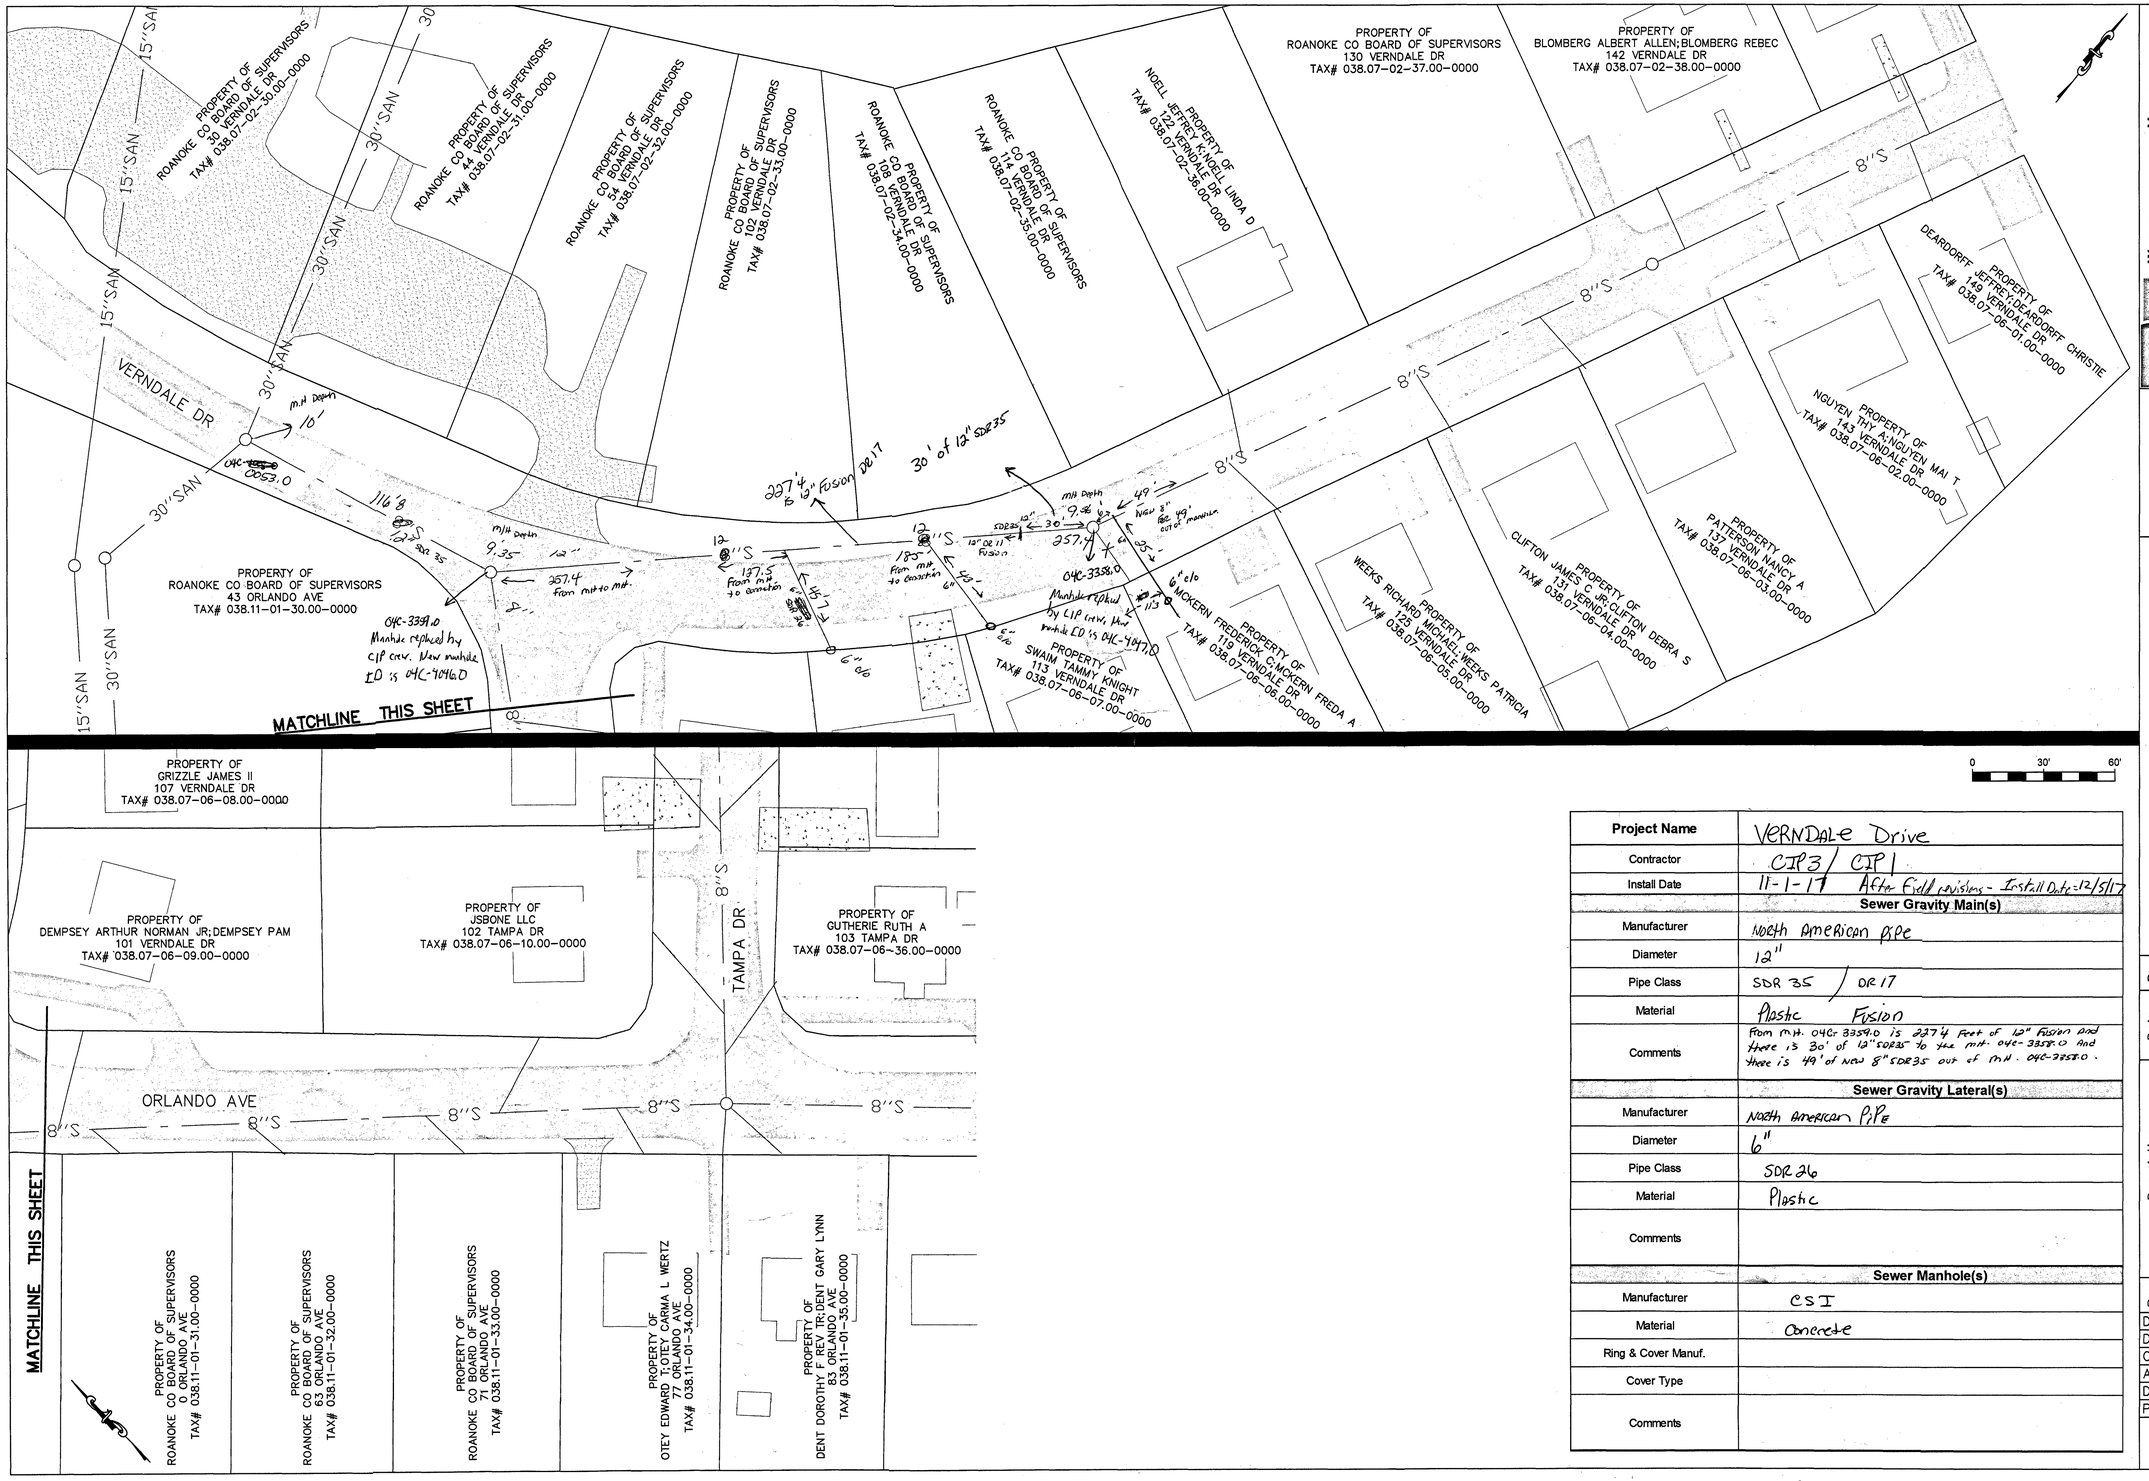

Project Name	VERNDALE Drive
Contractor	CIP3 / CIP1
Install Date	11-1-17 After Field revisions - Install Date=12/5/17
Sewer Gravity Main(s)	
Manufacturer	North American Pipe
Diameter	12"
Pipe Class	SDR 35 / DR 17
Material	Plastic Fusion
Comments	From mh. 049-3359.0 is 297.4 feet of 12" Fusion and there is 30' of 12" SDR35 to the mh. 049-3358.0 and there is 49' of new 8" SDR35 out of mh. 049-3358.0.
Sewer Gravity Lateral(s)	
Manufacturer	North American Pipe
Diameter	6"
Pipe Class	SDR 26
Material	Plastic
Comments	
Sewer Manhole(s)	
Manufacturer	CSI
Material	Concrete
Ring & Cover Manuf.	
Cover Type	
Comments	

WESTERN VIRGINIA WATER AUTHORITY
ENGINEERING SERVICES
601 S JEFFERSON ST, SUITE 300
ROANOKE, VA 24011
540-853-5700

VERNDALE DRIVE SEWER REPLACEMENT

BASEMAP

Rev	Description	Date	By

Designed:
Drawn: DRJ
Checked:
Approved:
Date: DEC 2017
Project:

1

Sheet 1 of 1
