



PHASE 2

1. REMOVE AND PLACE SIGNS AS SHOWN. PLACE BARRELS AND DIVERT AND MAINTAIN VEHICULAR AND PEDESTRIAN TRAFFIC AND SHOWN. MAINTAIN VEHICULAR ACCESS TO SECURE AREAS THROUGH NEW GATE #31. MAINTAIN PEDESTRIAN TRAFFIC THROUGH NEW GATE #30. MAINTAIN PARKING AS SHOWN. PROVIDE TEMPORARY PARKING AREA BETWEEN ACCESS ROAD #1 AND ACCESS ROAD #3 AS SHOWN. VDOT STANDARD 6" CRUSHER RUN AGGREGATE NO. 25 OR 26 SHALL BE PLACED ON TEMPORARY PARKING AREA. CRUSHER RUN AGGREGATE SHALL BE AS SPECIFIED IN VDOT SPECIFICATION SECTIONS 205 AND 512.
2. PLACE AVIATION BARRICADES AND TEMPORARY SECURITY FENCE AS SHOWN ON PLAN.
3. CONSTRUCT ACCESS ROAD #3, ACCESS ROAD #2, GA PARKING AREA, AND ENTRANCE #2.
4. INSTALL AND PUT IN SERVICE ALL REMAINING UTILITIES.
5. INSTALL GATES #28 AND #29 AND PERMANENT CHAIN LINK FENCE. REMOVE TEMPORARY SECURITY FENCE AND AVIATION BARRICADES. THIS OPERATION IS TO BE COMPLETED WITHIN 15 CALENDAR DAYS.
6. WITH THE EXCEPTION OF ENTRANCE #2 PAVEMENT, SURFACE ASPHALT WILL NOT BE PLACED UNTIL THE FINAL PROJECT PHASE.

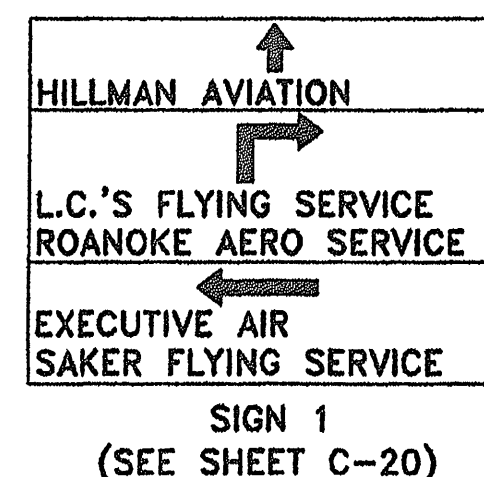

SIGN 1
(SEE SHEET C-20)

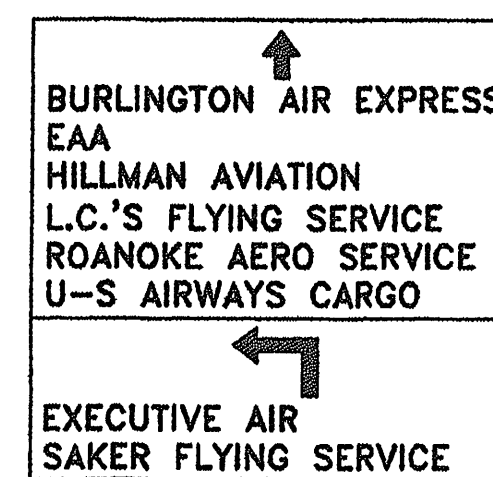

SIGN 2
(SEE SHEET C-20)

PHASE 3

1. PLACE BARRELS AND DIVERT AND MAINTAIN TUG TRAFFIC AS SHOWN. MAINTAIN A MINIMUM OF 10 FEET OF PAVEMENT FOR TUG TRAFFIC.
2. REMOVE AND PLACE SIGNS AS SHOWN. PLACE BARRELS AND DIVERT AND MAINTAIN VEHICULAR, TUG, AND PEDESTRIAN TRAFFIC AS SHOWN. MAINTAIN PARKING AS SHOWN. MAINTAIN ACCESS THROUGH GATES #28, 29, 30 AND 31.
3. GRADE AND CONSTRUCT THE REMAINING PORTION OF ACCESS ROAD #1 AND ACCESS ROAD #3. COMPLETE ALL CURB/ CURB AND GUTTER AND RESTORE ALL DAMAGED CURB.
4. COMPLETE FINAL SURFACE ASPHALT COURSE ON ALL NEW PAVEMENT.
5. INSTALL SIGNAGE.
6. APPLY PAVEMENT MARKINGS.

LEGEND

- UNDER CONSTRUCTION
- COMPLETED CONSTRUCTION
- VEHICULAR TRAFFIC
- PEDESTRIAN TRAFFIC
- TUG TRAFFIC
- AVIATION BARRICADES
- TEMPORARY CONSTRUCTION FENCE
- CONSTRUCTION BARREL BARRICADE

SEE SHEET C-19 FOR AVIATION BARRICADE
DETAIL, TEMPORARY SECURITY FENCE AND
BARREL DETAIL.

Mattern & Craig, Inc.
CONSULTING ENGINEERS - SURVEYORS
701 FIRST STREET, S.W.
ROANOKE, VIRGINIA 24016
(540) 345-9842
(540) 345-7691 FAX

DSGN	JMB	REV	DATE	DESCRIPTION	BY	APP
		Δ	9/6/2000	ADDENDUM #1	JLJ	MSA
DRAWN	JMC					
CHKD	MSA					

GENERAL AVIATION REHABILITATION - PHASE-IA
CONSTRUCTION PHASING PLAN
ROANOKE, VIRGINIA

**ROANOKE
REGIONAL
AIRPORT**

COMMONWEALTH OF VIRGINIA
MICHAEL S. AGEЕ
No. 15232
9/6/00
PROFESSIONAL ENGINEER

SCALE: 1"=60'
COMM. NO. 1442W
DATE: AUGUST 2000
SHEET C-4B
