

SUGGESTED MAINTENANCE OF TRAFFIC C-503

- 1(a) CONSTRUCT PAVEMENT ON PROPOSED RTE 221 LEFT OF CENTERLINE FROM STA 26+50 TO STA 32+50, MAINTAIN TRAFFIC RIGHT OF CONSTRUCTION
- (b) CONSTRUCT CONNECTION TO VIEW AVENUE IN A MANNER WHICH WILL ALLOW TRAFFIC TO BE MAINTAINED ON ONE HALF THE CONNECTION WHILE THE OTHER HALF IS BEING CONSTRUCTED

- 2(a) CONSTRUCT BOTH OUTSIDE PAVEMENTS FROM EDGE OF EXISTING PAVEMENT AS FOLLOWS: LEFT SIDE - STA 17+00 TO STA 26+50 & STA 32+50 TO STA 54+89.30 RIGHT SIDE - STA 17+00 TO STA 26+50 & STA 32+50 TO STA 55+23 FOR LIMITS OF STATIONS SHOWN ABOVE MAINTAIN TRAFFIC ON EXISTING PAVEMENT

- (b) CONSTRUCT THE PAVEMENT RIGHT OF RTE 221 CENTERLINE FROM STA. 26+50 TO STA 32+50, MAINTAIN TRAFFIC LEFT OF RTE 221 CENTERLINE.

- (c) CONSTRUCT THE FOLLOWING CONNECTION SIMULTANEOUSLY WITH THE OUTSIDE PAVEMENTS OF RTE. 221 WEDGEWOOD RD, HARRIS ST, BRANDYWINE AVE LT STA 35+52 TO, PINEVALE RD, CUSTIS AVE, & KEYNMORE AVE. EACH OF THE CONNECTIONS SHOWN ABOVE ARE TO BE CONSTRUCTED IN SUCH A MANNER AS TO ALLOW MAINTENANCE OF TRAFFIC ON ONE HALF THE CONNECTION WHILE THE OTHER HALF IS BEING CONSTRUCTED

- (d) THE REMAINING CONNECTIONS, WHICH ARE ALSO TO BE BUILT SIMULTANEOUSLY WITH THE OUTSIDE PAVEMENTS OF RTE. 221, ARE TO BE CONSTRUCTED AS FOLLOWS: CONSTRUCT BRANDYWINE AVE RT STA 35+62 TO 40 AND RE-ROUTE TRAFFIC TO PINEVALE ST OR HARRIS ST

- 3(a) CONSTRUCT THE REMAINING INSIDE PAVEMENT FROM STA 17+00 TO STA 26+50 & STA 32+50 TO STA 76+50 ON RTE 221 WHILE MAINTAINING TRAFFIC ON THE OUTSIDE PAVEMENTS

SUGGESTED MAINTENANCE OF TRAFFIC C-501

- 1(a) CONSTRUCT BOTH OUTSIDE PAVEMENTS FROM EDGE OF EXISTING PAVEMENT AS FOLLOWS: LEFT SIDE FROM STA. 55+10 TO STA. 76+50; RIGHT SIDE FROM STA. 54+84 TO STA. 76+50.


- (b) CONSTRUCT VALLEY FORGE AVE. TO MAINTAIN TRAFFIC ON ONE HALF OF THE CONNECTION WHILE THE OTHER HALF IS BEING CONSTRUCTED.

- 2(a) CONSTRUCT RELOCATED RTE. 682 FROM STA. 10+32.31 TO STA. 14+50.3 & LEFT OF RELOCATE & 14+50.3 TO STA. 19+55 WHILE TRAFFIC IS MAINTAINED ON EXISTING RTE. 682.

- (b) CONSTRUCT PROPOSED RIGHT SIDE OF KENMORE AVE. WHILE MAINTAINING TRAFFIC ON EXISTING SURFACE, & RESURFACE EXISTING SURFACE UNDER TRAFFIC.

3. CONSTRUCT WESTMORLAND DRIVE & RE-ROUTE TRAFFIC TO VALLEY FORGE AVE.

4. CONSTRUCT REMAINING PORTIONS OF RTE 221 & RTE 682 WHILE MAINTAINING TRAFFIC ON EARLIER CONSTRUCTED PORTIONS.

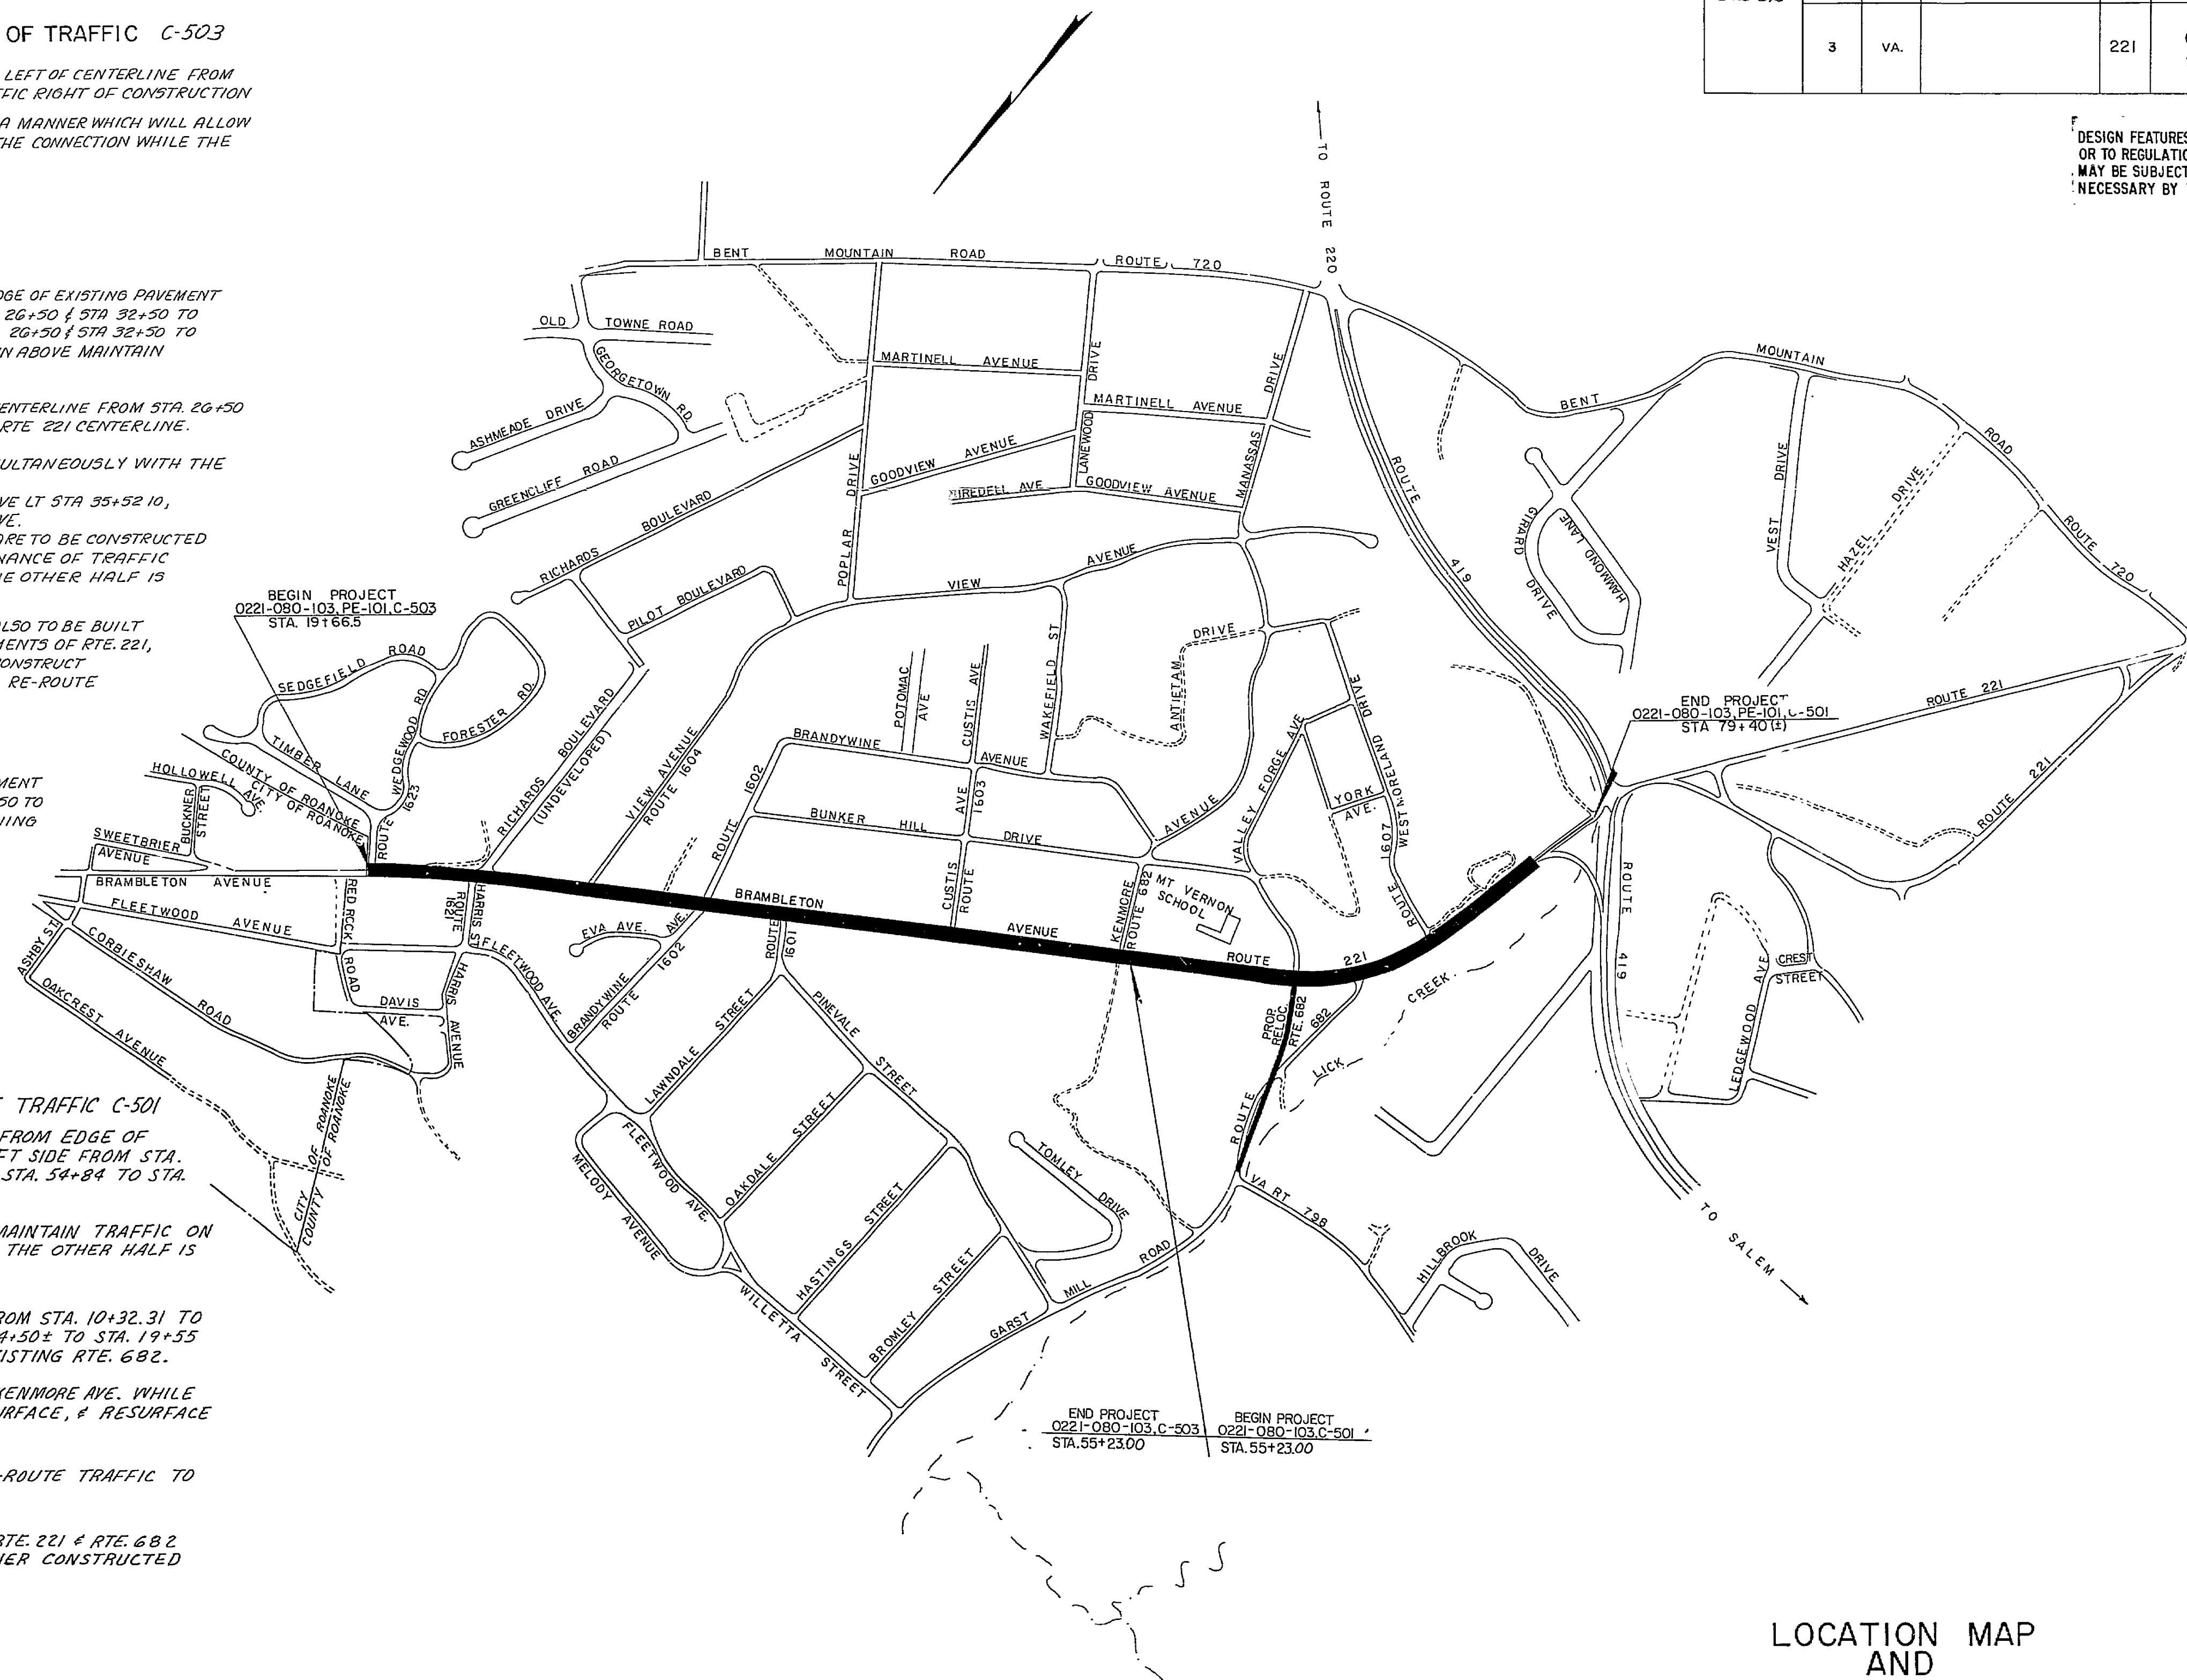

| REVISED | FHWA REGION | STATE | FEDERAL AID | ROUTE | STATE PROJECT                     |
|---------|-------------|-------|-------------|-------|-----------------------------------|
| 6-28-82 | 3           | VA.   | PROJECT     | 221   | 0221-080-103, C-50. R/W-201 C-503 |

DESIGN FEATURES RELATING TO CONSTRUCTION OR TO REGULATION AND CONTROL OF TRAFFIC MAY BE SUBJECT TO CHANGE AS DEEMED NECESSARY BY THE DEPARTMENT.

LOCATION MAP AND MAINTENANCE OF TRAFFIC

| PLAN NO. | PROJECT      | FILE NO. | SHEET NO. |
|----------|--------------|----------|-----------|
| A        | 0221-080-103 | RC-5426  | 1-A       |

